


REQUEST FOR UNDERGROUND CIVIL CONTRACT CONSTRUCTION & INSPECTION

UCC Ref#	Approvers Name (P-Print)		Title	Signature	Date
District Name: MENIFEE	MARK MESA		OS	06/12/19	
SAP Order# TD1536732	Notification#: 409764564				
DIMP: ☐ CAPITAL ☒ O&M	DIMP Due Date: 6/26/19	MAT Code:			
Requestor: Michael Elardo	Pax:	Cell: 951-595-5270			
Description of Work: Need civil crew to dig pole hole with sono-tube for 45' C2 pole, helicopter set on Friday 6/14.					
Location: 2258 Post Rd.			City: Perris		
Structure#:2090580E			Inventory Map No: 592-1680-2 (must include readable map w/pkg)		
Circuit: Pawnee 12kv		Substation: Gavilan		Thomas Guide:	
12kv		(must include readable map w/pkg)			
Permit Required: ☐ Yes # _____ (Must be included in package), ☒ No			Easement Required: ☐ Yes ☒ No		
Reason: ☒ Private Property, ☐ Other *: _____			Easement Secured: ☐ Yes ☐ No		
NOTE: All permits including Blankets must be included in package at time of submission.					
* If "OTHER", PROVIDE COMPLETE, VALID REASON					
Category: ☐ Customer Out of Power / Immediate Danger to the Public ☐ Outage or Electrical Crew Schdl Date Related CCM/Requestor Name: _____ Ph#: _____ ☐ 3rd Party Connection Contact Name: _____ Ph#: _____ ☐ All Other					
Proposed Civil Construction Start Date: 06/12/19			Required Civil Completion Date: 06/13/19		
Emergency Reason:			Crew Meet Date:		
MATERIAL TYPE	QUANTITY	UNIT	UNIT COST	EXTENDED COST	
Labor-2 man		8 hours	220.00	1760.00	
Sonotube	1		200.00	200.00	
42% overhead loader				823.20	
			TOTAL ESTIMATED COST: \$ 2783.20		
Documentation of Actual Cost Required: ☒ No, ☐ Yes Send to: Name: _____ Pony: _____					
For Underground Construction Use Only					
MAT Code:	Agreement#	PO#	PO Line Item#		
SCE Inspector:		Invoice No.:	Amount		
Contractor:	Contractor Job No.:		\$		
Construction Start Date:			\$		
Construction Completion Date:			\$		
Recording Required: ☐ No ☐ Yes, Completed on:	Total Actual Cost		\$		
Job in Click: ☐ Yes ☐ No QA Included: ☐ Yes ☐ No	Actual Date Cost Submitted:				
Construction Comments:					






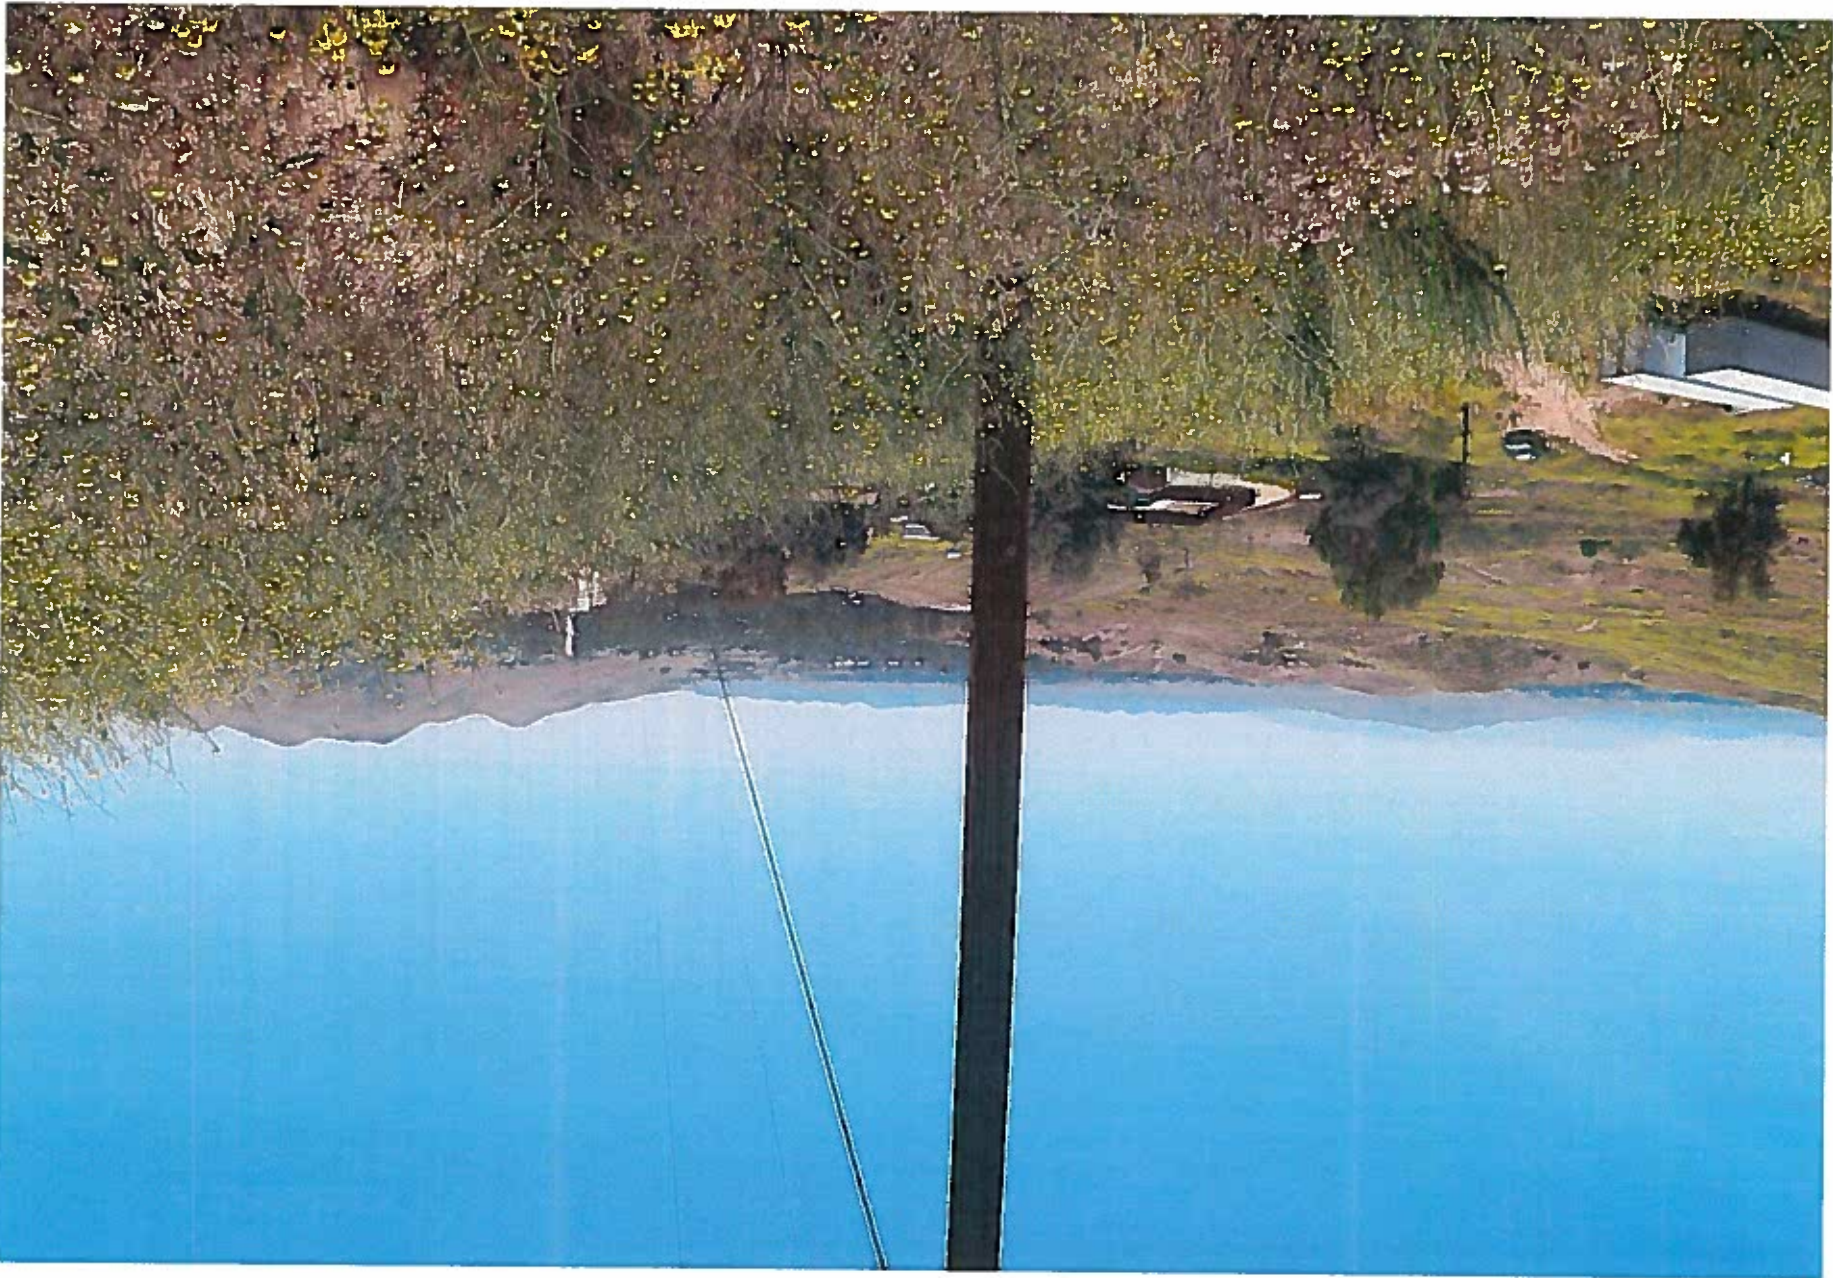

Comments

[illegible]

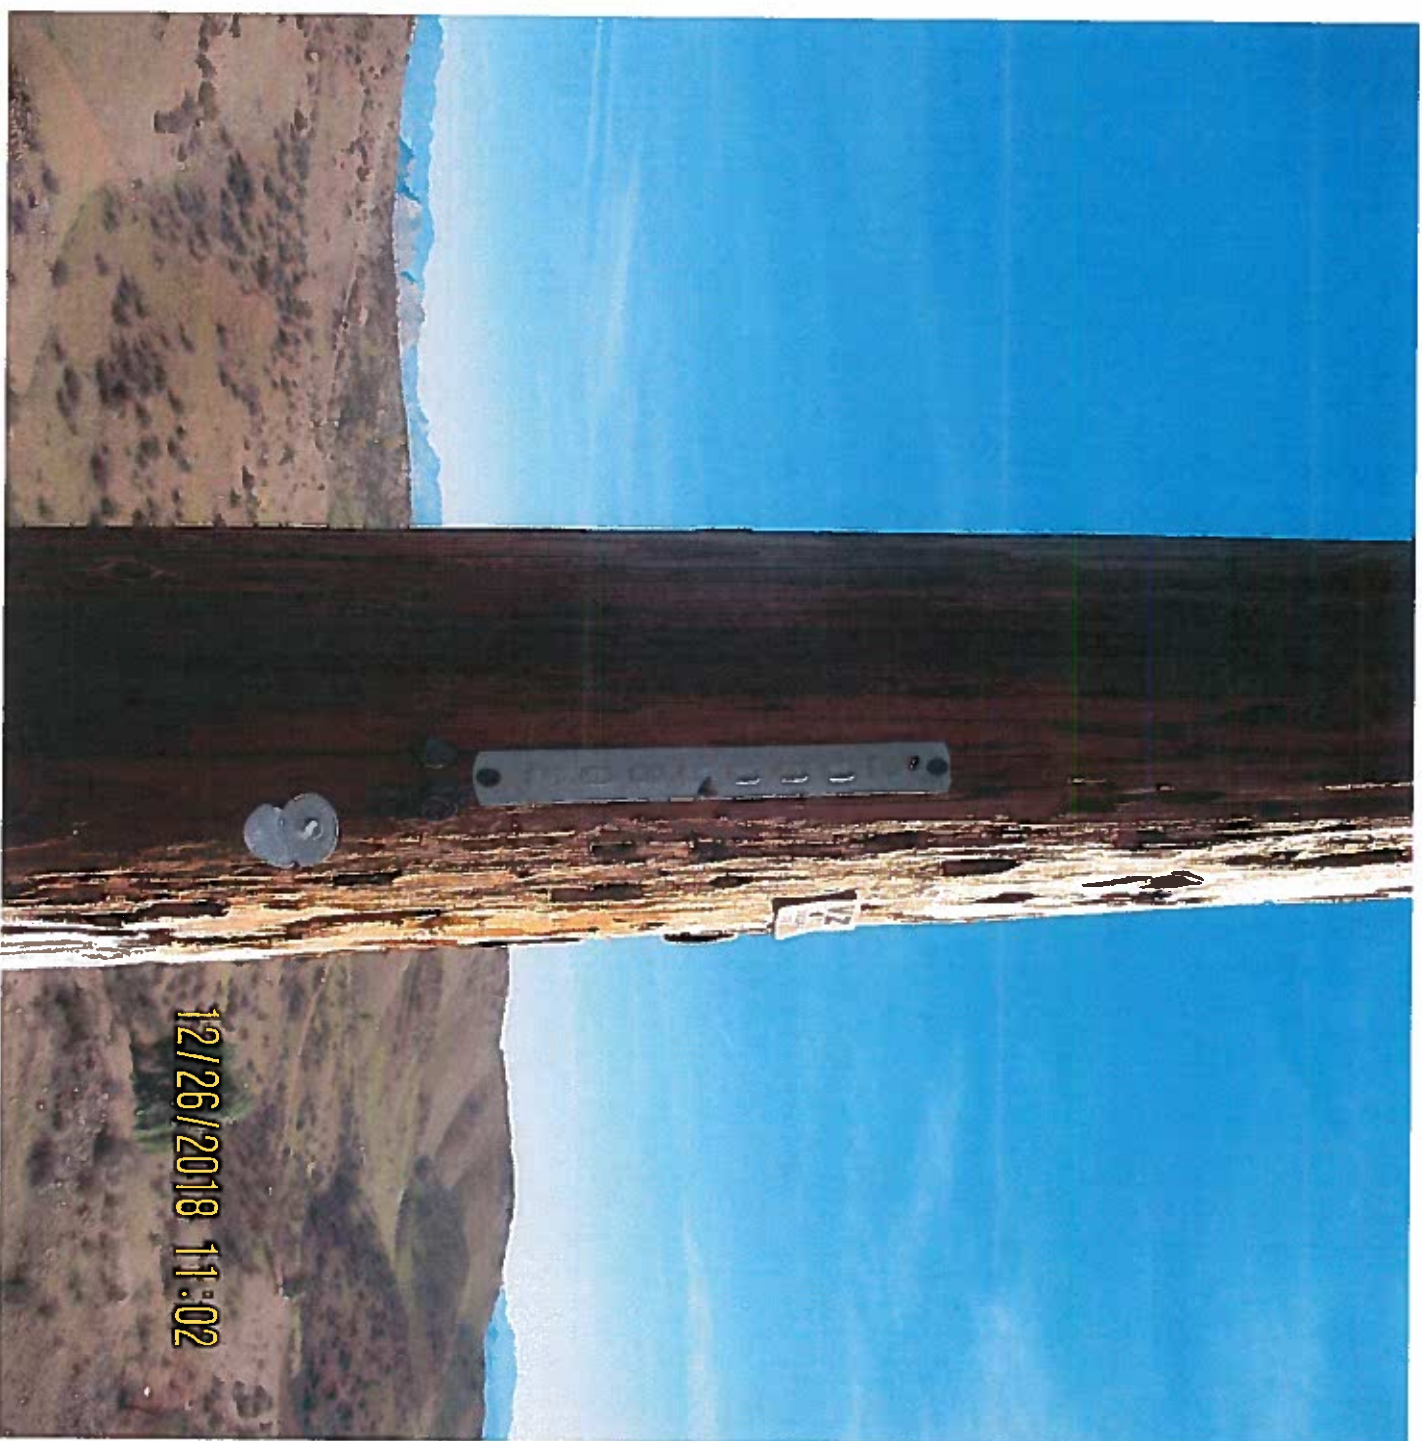

Luis - 323-697-6705

PAO Lock Code - 4762
2258 Post Rd - FLY YARD SEC

T 4 S
SE

PROJECT REQUIREMENTS

- EDISON AGREEMENT REC'D ☐
- PERMITS REC'D ☐
- CONVEYANCE LETTER REC'D ☐
- JPA REC'D ☐
- RENTER NOTIFICATION REC'D ☐
- ENVIRONMENTAL CLEARANCE REC'D ☐
- CSD 140 (TLM) REC'D ☐
- TRAFFIC CONTROL REC'D ☐

2

G2

IN: 2 0 9 0 5 8 0 E

45'

IN: POLE-45' CLASS 2 WOOD FULL TREAT - D-IN
IN: XA SINGL TRN HD COMP ID' W/ BKT - D-IN
IN: 2- INS GLASS & PIN 12KV TIE TOP#4ACSE - D-IN
IN: XA SINGL DE HD COMP ID' W BKT - D-IN
IN: 2- INS POLY DE 12KV HDT SHDE #4 & 1/0 - D-IN
2- 3/8" BOLT TO CUT & KICK ✓ PTD
3- HELICOPTER SET

RM: 40' WOOD C5 POLE - D-RM
RM: 2- INS GLASS & PIN 12KV TIE TOP#4ACSE - D-RM
RM: XA SINGL FB 5' STEEL PINS - D-RM
RM: 2- INS GLASS & PIN 12KV TIE TOP#4ACSE - D-RM
RM: XA SINGL FB ID' WOOD PINS - D-RM

Cut in Isolators
Load Drop too!


NOTIFICATION# 4D9764564

VICINITY MAP




1931400E 1/OAT+120
120/240
13415

PLANNER: WILL HUERTA		JOB NAME: REPLACE PRIMARY POLE - DCI		FOREMAN:		DISTRICT: MENIFEE - 77	
DWO:		JOB LOCATION: POST RD W/S 2.660' W/O BALDWIN RD		TRUCK: P/E:		DATE SENT TO R/W: DIST. SKETCH #	
SAP NO.:		TLM-CSD 140 REQUIRED YES NO		DRAWN BY:		INV. MAP NO.'S	
JPA NO.: 40029807		GRID NO. B5		PHONE NO.:		592-1680-2	
THOMAS MAP		EXIST. PROP. SIZE KVA CUST. LOAD		INV. MAP NO.'S			
RELATED NO. TD1536732		VOLTAGE DROP P.R. CIRC.: PAWNEE 12KV		INV. MAP NO.'S			

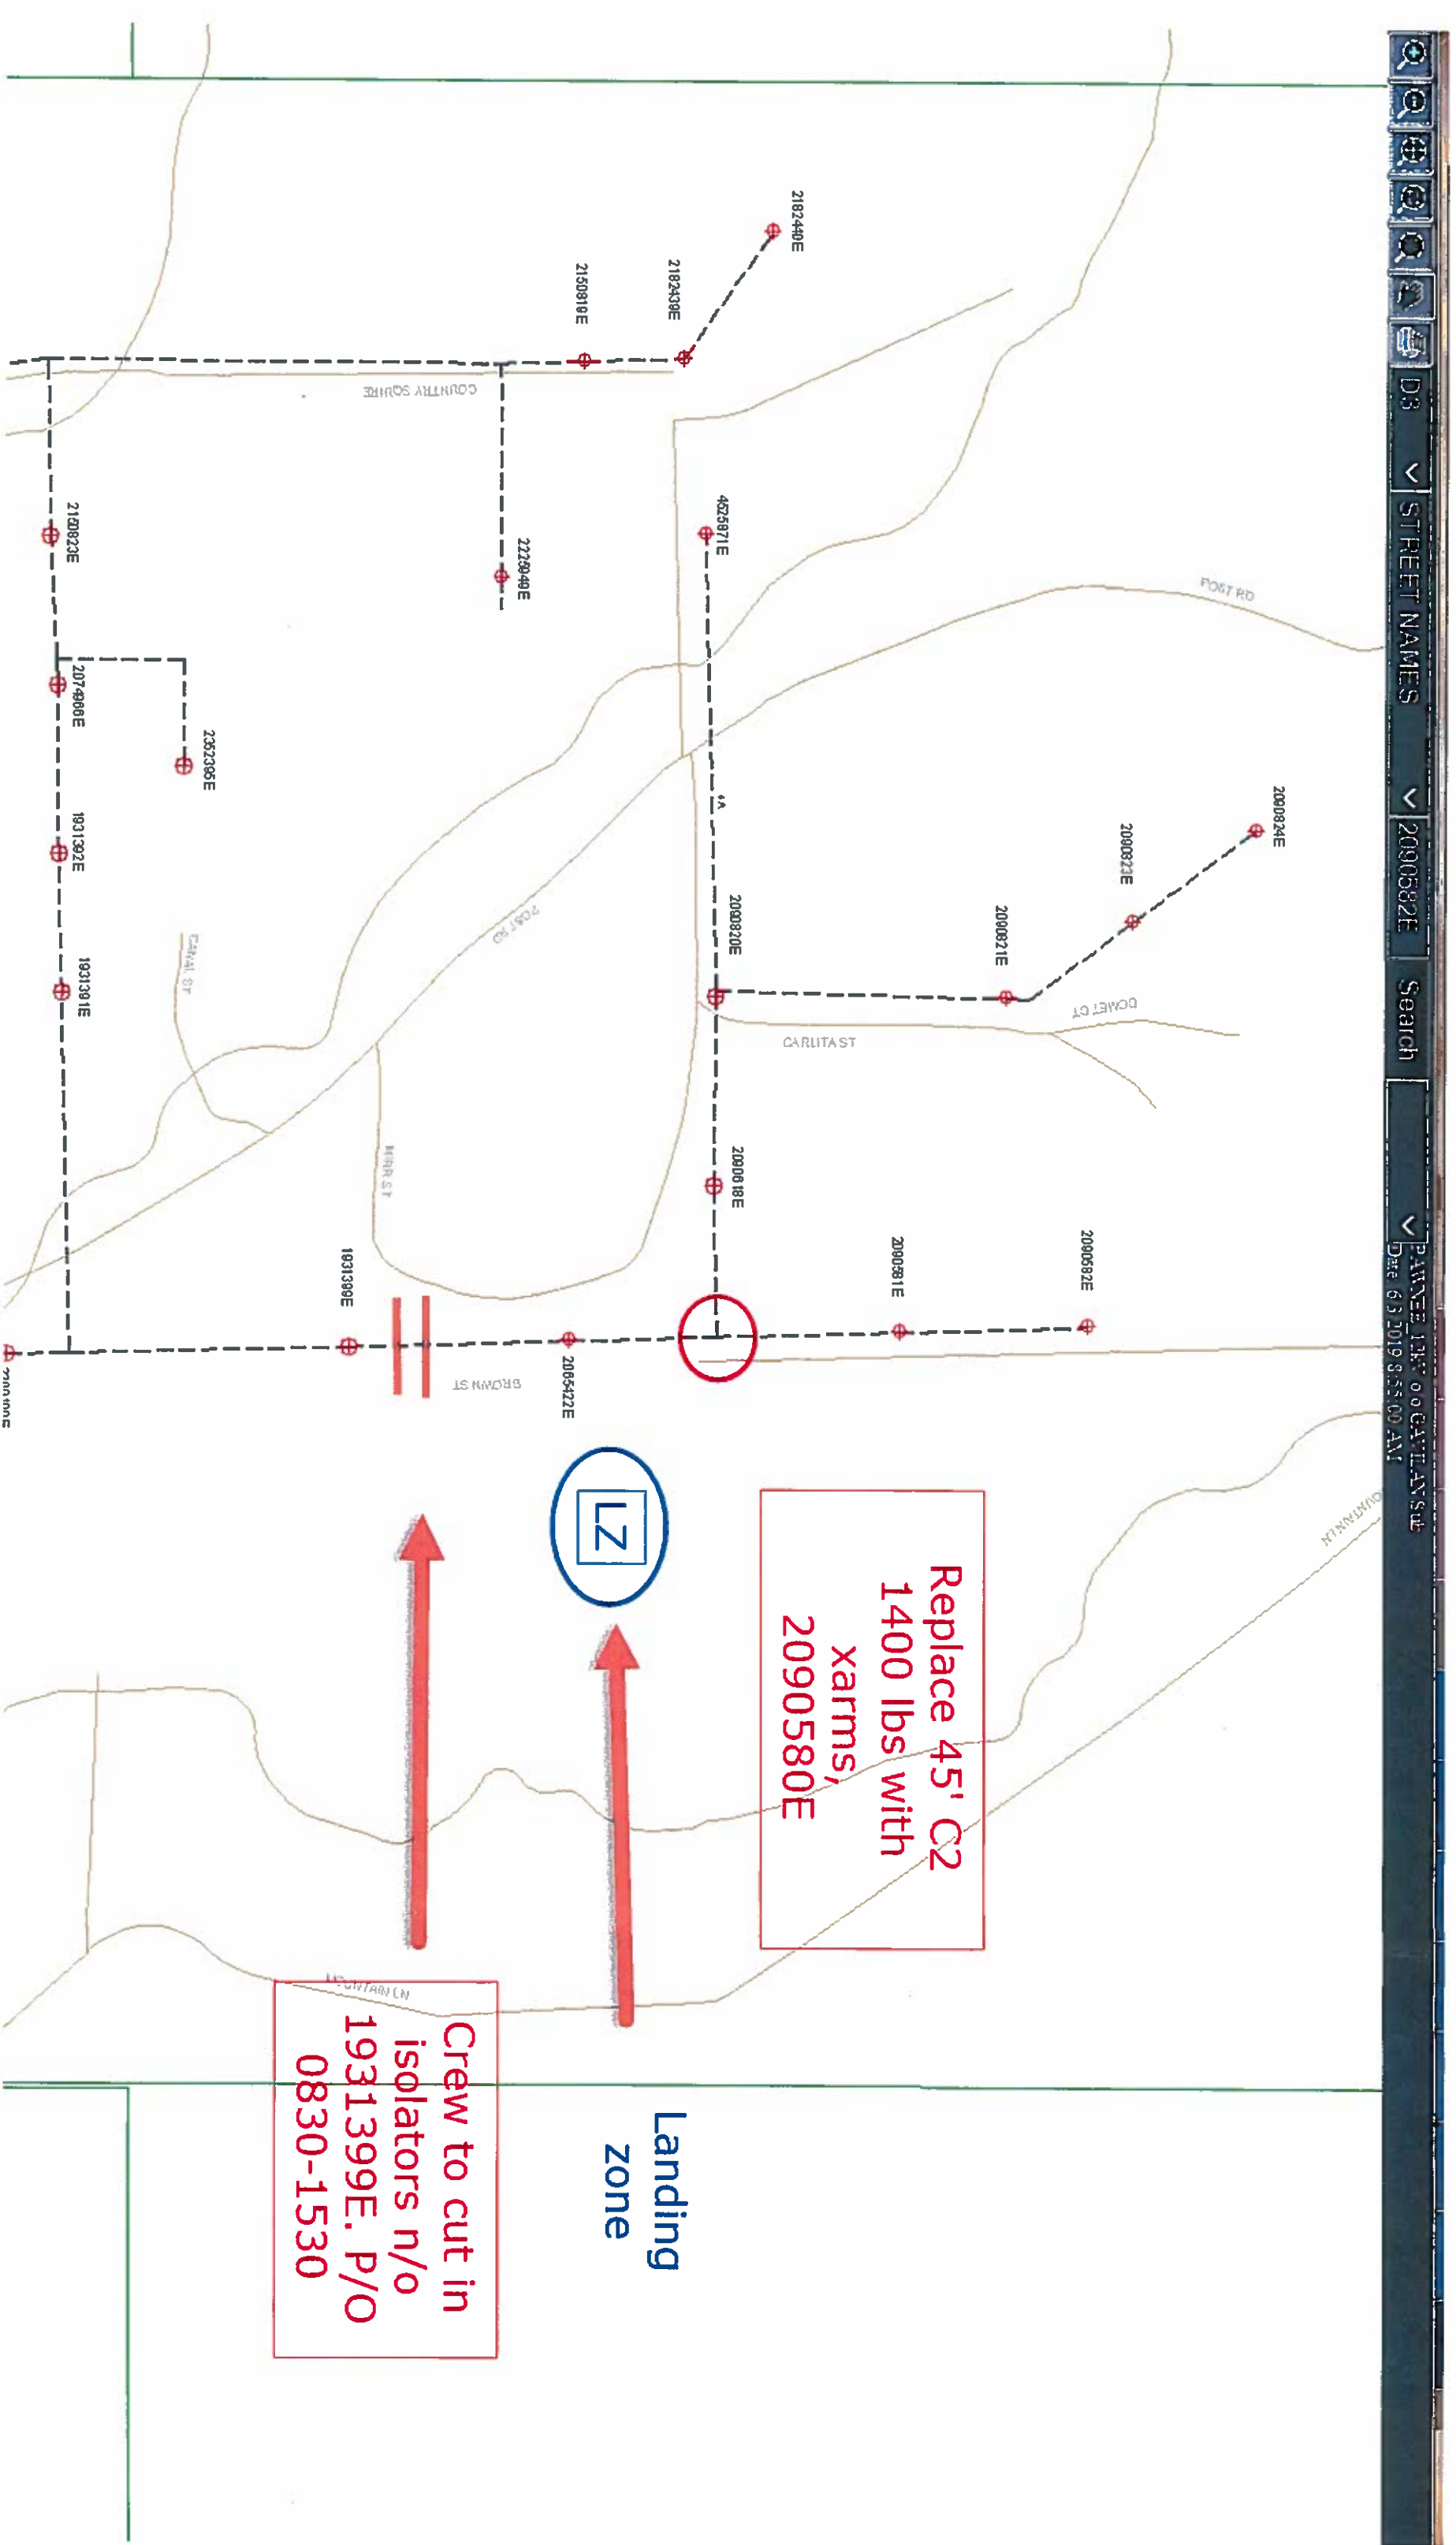

Pole 2090580E

Landing Zone.

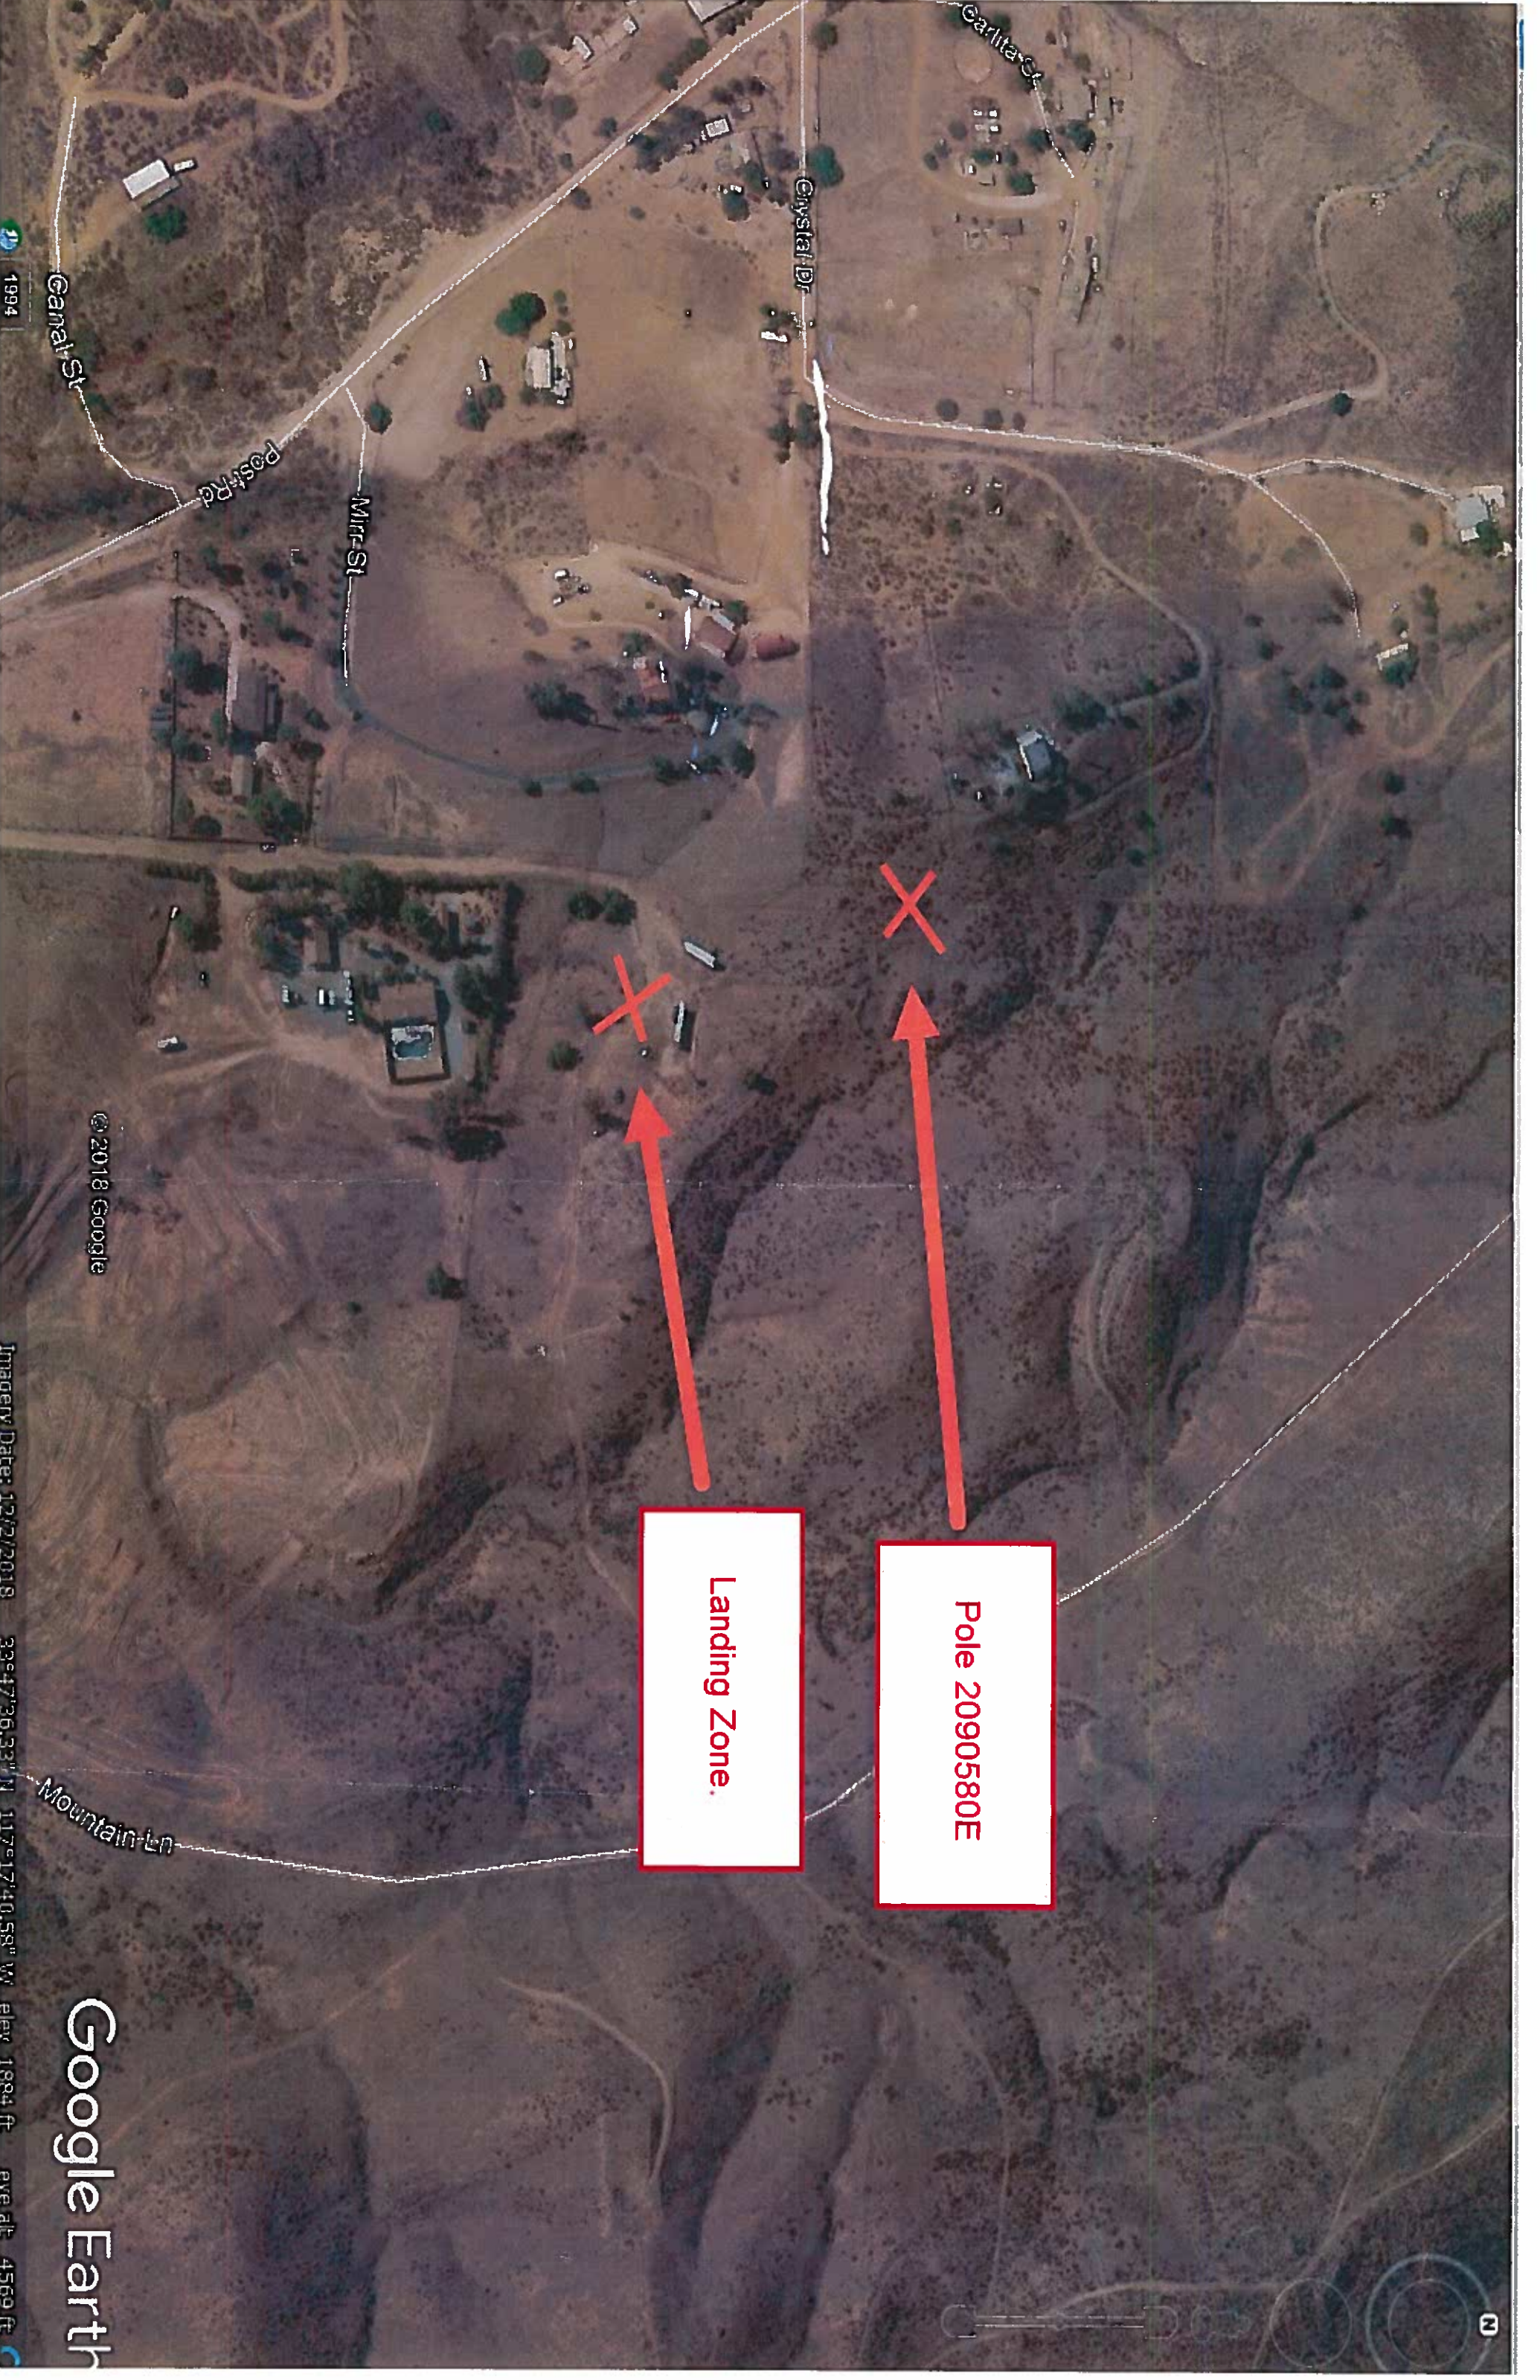


© 2018 Google

Google Earth

1994

Imagery Date: 12/21/2018 33°47'36.33"N 117°17'40.58"W elev 1894 ft avel 4569 ft

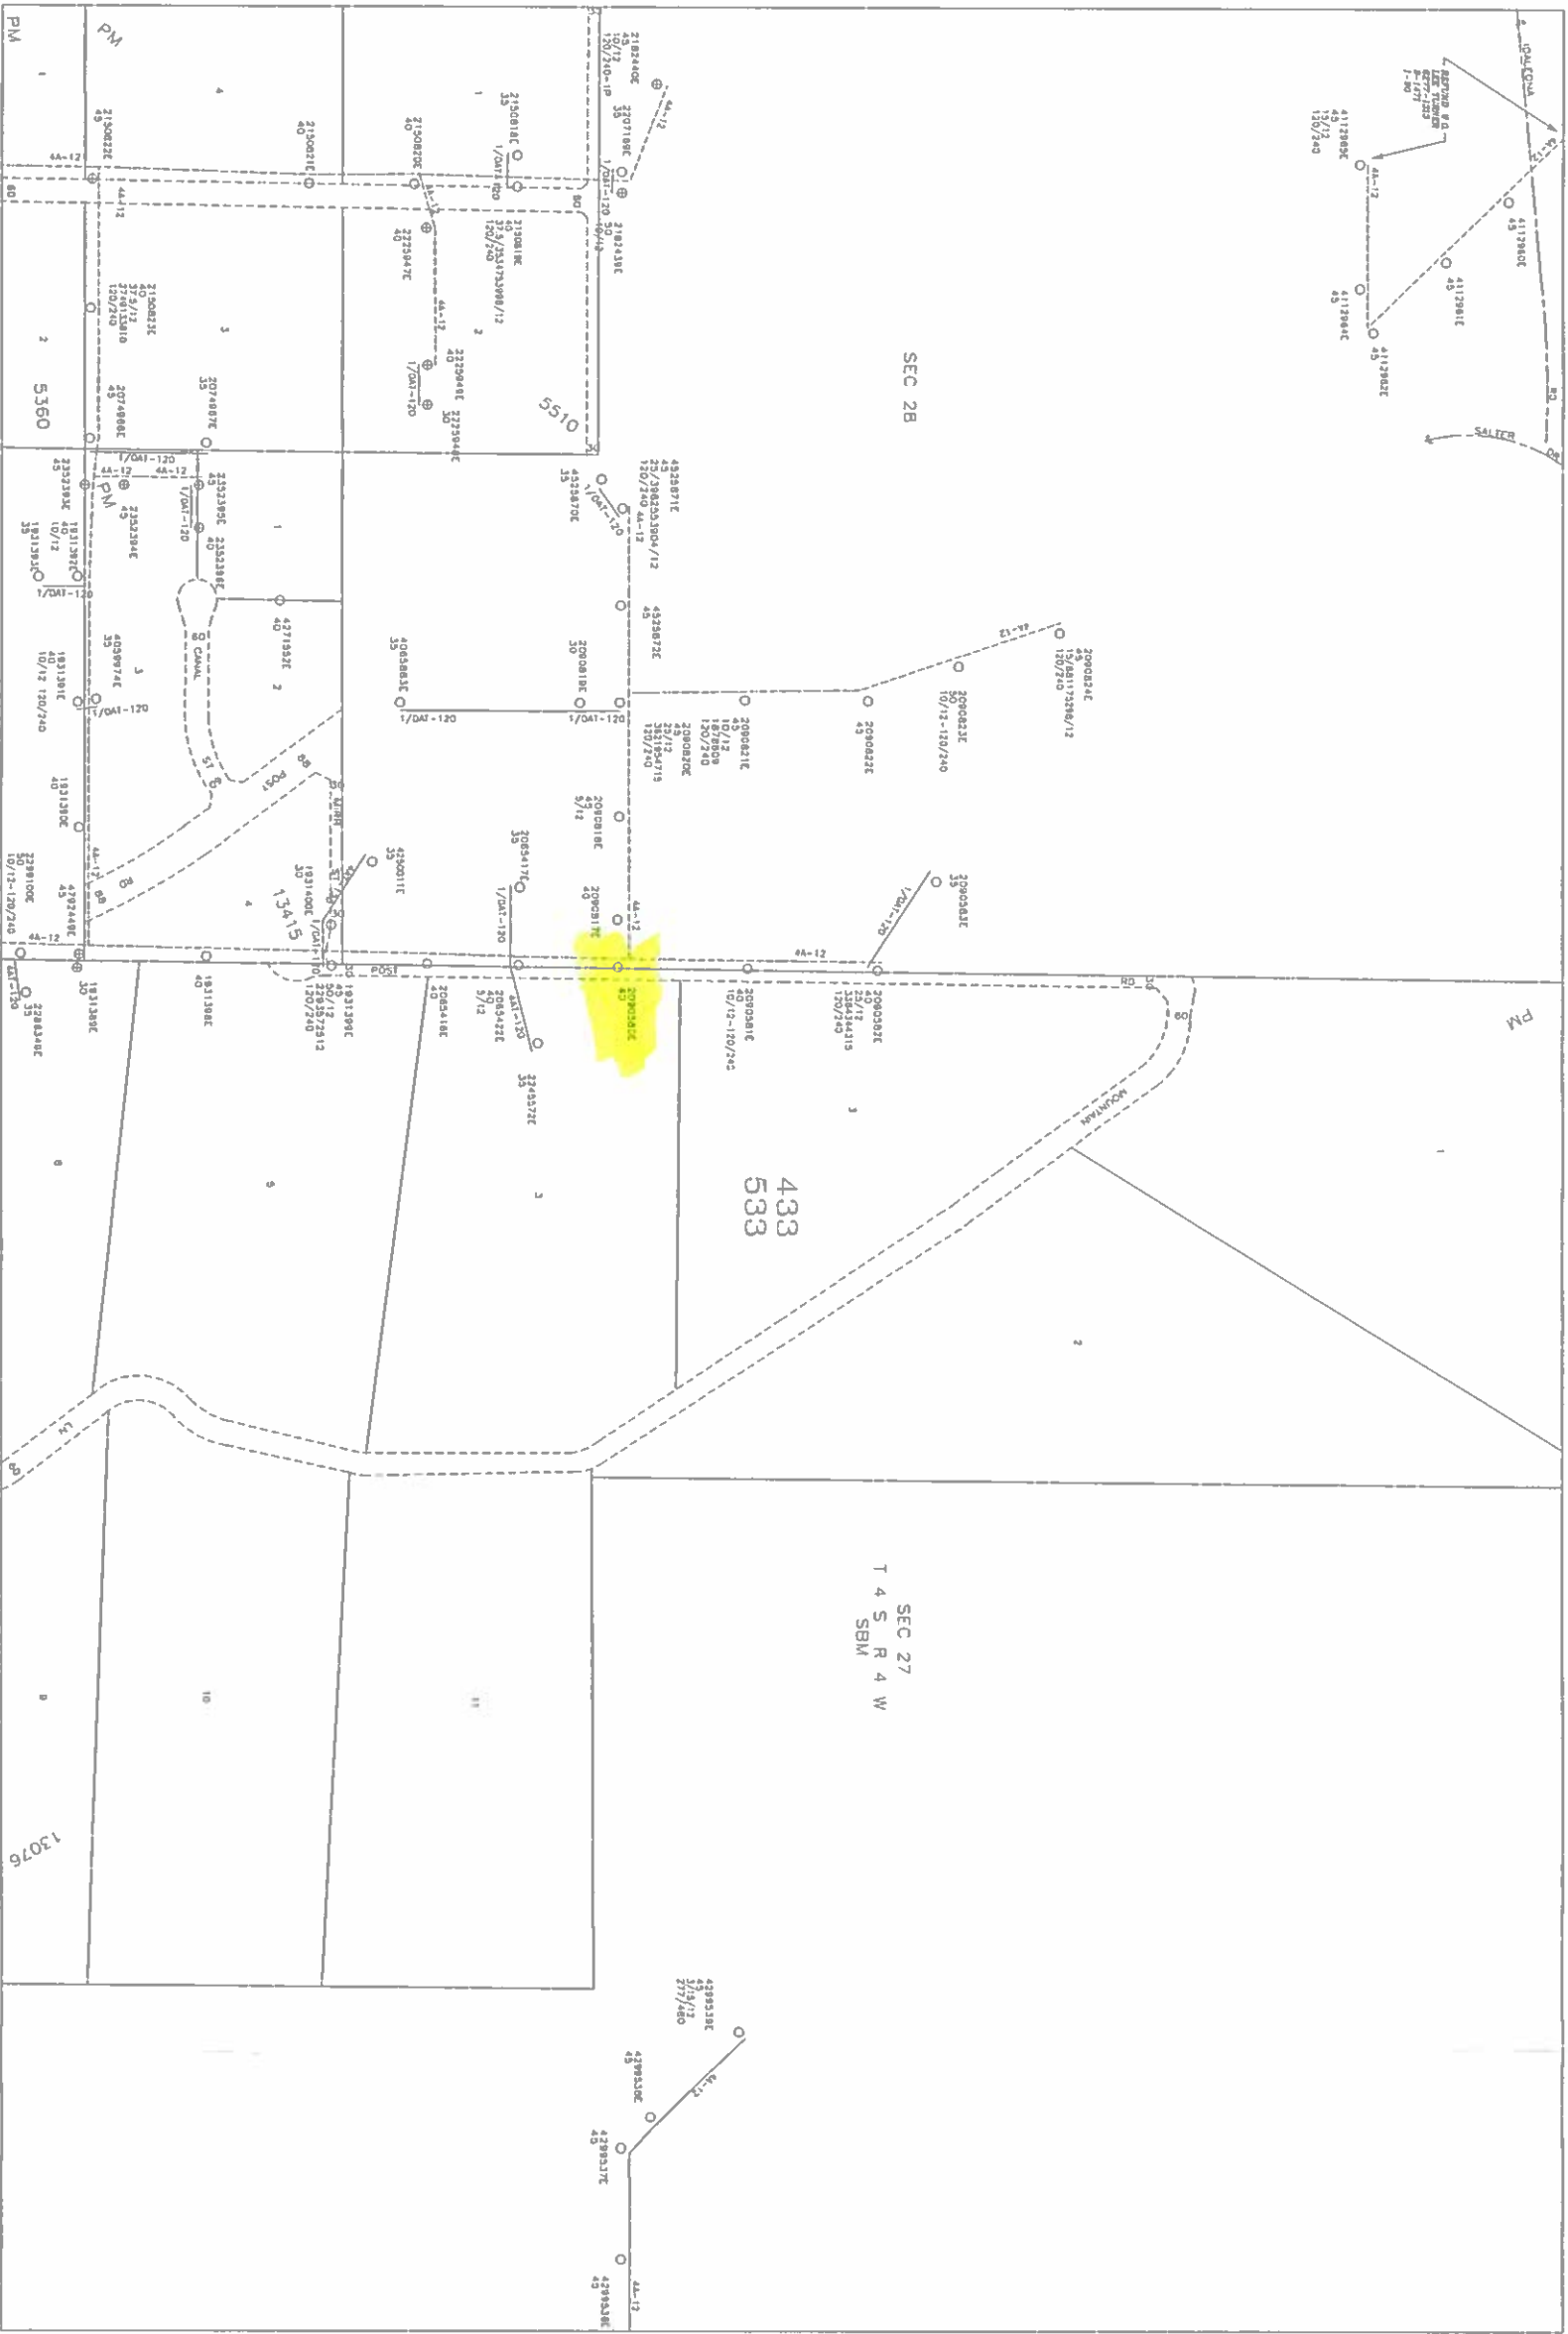

592-1674-2

592-1686-1

594-1688-1

1,680,000
20N4
592,000

1-17 EQUIL 12-13 GAGE
3-12 CIVIL 12-13 GAGE

590-1680-1 590-1683-1

SCALE IN FEET
0 300 600 900
SCALE IN METERS
0 100 200 300

MENEFEE

