

GUARDIAN

HELICOPTERS, INC.

HELICOPTER LIFT OPERATIONS SAFETY BRIEF CHECKLIST

PRIOR TO BEGINNING ANY HELICOPTER OPERATION A THOROUGH SAFETY BRIEF WILL BE CONDUCTED UTILIZING THE FOLLOW CHECKLIST: *Avila Bch / Morro Bay*

- ☐ SAFETY BRIEF SIGN IN *PGE 21-01861*
- ☐ GHI CREW INTRODUCTION *N4476H HEC / Mark Ball / Airchair*
- ☐ IS A TRANSLATOR REQUIRED *NON CAP*
- ☐ WORK STOP AUTHORITY *(2) L2s*
- ☐ DESIGNATE A 911 CALLER
- ☐ IDENTIFY CLOSEST EMERGENCY MEDICAL SERVICES
- ☐ CREW FATIGUE AND HYDRATION
- ☐ HELICOPTER LIFT LIMITATIONS
- ☐ HAZMAT WILL OR WILL NOT BE CARRIED ON THE HOOK
- ☐ NON GHI EMPLOYEES WILL NOT APPROACH HELICOPTER WITH ROTORS ENGAGED
- ☐ HELICOPTER HAZARD AREA (TAIL/MAIN ROTOR)
- ☐ EFFECT OF ROTOR DOWN WASH ON LOAD

DUST MASK: BURN AREA, DUST, POLLEN EXPOSURE

- ☐ HELICOPTER DOOR REMOVAL AND FIRE EXTINGUISHER LOCATION
- ☐ PPE REQUIREMENTS (GLOVES, EYE PROTECTION, HARD HAT WITH CHIN STRAP)
- ☐ PILOT/GROUND CREW COMMUNICATIONS/ LOST COMMUNICATIONS

PROCEDURES

- ☐ POTENTIAL STATIC CHARGE CAUSED BY HELICOPTER
- ☐ SITE PLAN / FLIGHT PATH
- ☐ FALL, PINCH, CRUSH DANGER POINTS
- ☐ RIGGING OPERATIONS CONNECTING AND DISCONNECTING CRANE HOOK AND SPREADER BAR HOOK
- ☐ PROPER SECURING OF EQUIPMENT / TOOLS IN SUPER SACK AND ON LONG LINE
- ☐ STREET CLOSURE / EVACUATION USE DIAGRAM TO ENSURE ALL HOMES ARE CLEAR
- ☐ NO CELL PHONES OR CAMERA USED BY GROUND CREW



HELICOPTER HEC OPERATIONS SAFETY BRIEF CHECKLIST

PRIOR TO BEGINNING ANY HELICOPTER HEC OPERATIONS A THOROUGH SAFETY BRIEF WILL BE CONDUCTED UTILIZING THE FOLLOW CHECKLIST THIS DOES NOT SUPERSEDE INITIAL HEC TRAINING REQUIREMENTS

- ☐ CONDUCT STANDARD HELICOPTER LIFT SAFETY BRIEF PRIOR TO HEC SAFETY BRIEF
- ☐ HEC SAFETY BRIEF SIGN IN
- ☐ INITIAL HEC TRAINING VERIFIED ISSUE STICKER DISPLAYED ON HELMET
- ☐ WORK STOP AUTHORITY
- ☐ PPE REQUIREMENTS (HELMETS, EYEWEAR, GLOVES AND FOOTWEAR)
- ☐ HARNESS, FITMENT, CONDITION AND LOAD LIMIT
- ☐ PROPER USE OF ATTACHMENT EQUIPMENT (CARABINERS)
- ☐ BUDDY /SELF CHECK
- ☐ COMMUNICATIONS REQUIREMENTS VIA RADIO OR HEAD AND HAND SIGNALS (RADIO WILL BE TETHERED OR SECURED)
- ☐ NO EQUIPMENT WILL BE TRANSPORTED DURING HEC
- ☐ HEC SHORT HAUL OPERATIONS PLAN, DAILY MISSION
- ☐ INSERTION POINT AND AREA HAZARDS
- ☐ HEC ATTACH ZONE AND WAITING AREA
- ☐ EMERGENCY PROCEDURES; ENGINE FAILURE, TR FAILURE, HOOK FAILURE, LINE ENTANGLEMENT)
- ☐ NO CELL PHONE OR CAMERA USED DURING HEC

Pilot:

Location:**Mission:****Aircraft:**[illegible]

AIRCRAFT	ENVIRONMENT	EXTERNAL LOAD
☐ Approach and departure ☐ Main/tail rotor hazards ☐ Safe cargo loading/unloading ☐ Loose articles: - Aircraft & LZ ☐ Hearing protection ☐ Door/seatbelt operation ☐ Headset/helmet/intercom ☐ Air-sickness ☐ In-flight emergencies Establish who will call 911 ☐ Location of: o First aid/survival kit o Fire extinguisher o Fuel and battery shut off procedure o Radios, ELT, SAT Phone ☐ Fueling Operations: - Duties & Safety Issues	☐ Weather conditions ☐ Wind direction ☐ Fuel ☐ Gross weight ☐ Terrain ☐ Landing zone hazards ☐ Density altitude ☐ Noise abatement ☐ Congested area plan ☐ Traffic/crowd control CRM ☐ COMMUNICATION IS CRITICAL ☐ Standardized language ☐ "Code Red" phrases ☐ Sterile cockpit ☐ Flight following/radio procedures ☐ Possible tasks for crew, e.g., switch/tune radios, maps ☐ Hazard awareness, e.g., birds, other hazards ☐ STOP work policy ☐ Re-brief in case scope changes ☐ <u>IMSAFE Acronym</u> Pilot fatigue mitigation must be briefed prior to work	☐ Ground crew PPE ☐ Long Line & Rigging Equipment Inspection ☐ Communication: Use of headset for lineman communicating with pilot ☐ Head/Hand Signals ☐ Pole set procedures: Brief how pole will be secured: 1) Taglines 2) Pikes 3) fill dirt ☐ Steps on pole ☐ Remote hook operations ☐ Ground crew hook up procedures ☐ Static discharge ☐ Emergency flyaway procedures ☐ Long line clearance (6'- 25'- 150% rule) ☐ No person under load ☐ Ground crew safety zone ☐ Pole removal with potential snag issues must be discussed ☐ Nylon straps (wood vs. glass) ☐ Load ratings (7:1 minimum) ☐ Dry Run/Play by play pole set Procedures ☐ Induced Voltage from: - Adjacent circuits, Underbuild, Parallel circuits etc. ☐ In case of Non-Company ground crew: Rigging procedures must be briefed ☐ No cell phone/camera use during external loads ☐ Essential crew only

21-01861 Request Summary



Requestor	Michael J Roben	Request Date	08/17/2021
LAN ID	mjrb	Work Type	Lift Work
Phone	(805) 546-5244	Lift Work Type	HEC -
Cell	(805) 588-0702	For Contractor	Non-Energized
LOB	Electric Transmission		No
	Line		
Vendor	Guardian Helicopters		

Work Dates

08/30/2021 - 08/31/2021 AS350B2

Approver	Superintendent Pete M Dominguez (pxd1)	PXD1@PGE.COM	(C) (805) 459-6255
Foreman	Jacob M Kristy (j1k7)	(P) (661) 340-5833	(C) (661) 340-5833

Scope of Work SAN LUIS OBISPO COUNTY
 MORRO BAY-MESA 230KV
 DIABLO-MESA 230KV
 CAP - NIL
 DISPATCH NOTIFICATIONS - DCP

USFS/NATIONAL PARK TERRITORY - NIL
 NOTIFICATIONS MADE - NIL

SCOPE - We have 2 dead-end 230 towers to reinsulate on the Morro Bay Mesa 230kv line. We will use the aircraft to transport the hardware and lineman to each tower to reinsulate them. The 230 tower work will be on the 8/30 and we will also use the aircraft to install marker balls at DCP off of the Diablo Mesa 0/1 to a pole just East of DCP 230kv yard.

LZ/WORK LOCATION INFORMATION -
 LZS OK, NO OBSTRUCTIONS. LZS VERIFIED FOR TYPE 3 AIRCRAFT - 100FT. WORK
 LOCATIONS OK, NO OBSTRUCTIONS.

REQUESTOR TO ENSURE TRAFFIC MITIGATION IS IN PLACE AS NEEDED.

Daily Information

08/30/2021

Asset Category: LIGHT

Asset Type: AS350B2

Locations

08:30 - LZ	Upper Los Baros LZ	35 06.76'N 120 31.19'W	<no headquarters>	<no county>
-------------------	--------------------	---------------------------	-------------------	-------------

Dust/Snow Mitigation Plan: Surface is composed of asphalt, concrete or gravel.

--- - Work Location

20101 MORRO BAY-MESA 230 KV	35 07.05'N 120 31.55'W	Line #: 26/112	PISMOBCH	<no county>	950 ft
-----------------------------	---------------------------	----------------	----------	-------------	--------

21-01861 Request Summary

Dust/Snow Mitigation Plan:

Surface is composed of asphalt, concrete or gravel.

--- - Work Location

20101 MORRO BAY-MESA 230 KV

35 07.87'N
120 32.49'W

Line #: 24/108

PISMOBCH

<no county>

500 ft

Dust/Snow Mitigation Plan:

Est. Use Hours	8.00	Vendor	Guardian Helicopters
Contract	PSPS GUARDIAN (AS350B2)	Over Water	No
Fuel Truck	Yes	Cargo Weight	650.0 lbs
Special Equipment	HEC Gear	Billing Number	31501671 100%
Comments	This first day will be using platforms for the 230kv reinsulates due to both are double dead-ends. The rest of the material will be pretty standard.	Req. Notifications	Air to Air

21-01861 Request Summary

08/31/2021

Asset Category: LIGHT

Asset Type: AS350B2

Locations

08:30 - LZ	DCPP LZ	35 12.74'N 120 49.69'W	<no headquarters>	<no county>
-------------------	---------	---------------------------	-------------------	-------------

Dust/Snow Mitigation Plan: Surface is composed of asphalt, concrete or gravel.

--- - Work Location

20031 DIABLO-MESA 230 KV	35 13.05'N 120 51.07'W	Line #: X0/1	PISMOBCH	<no county>	500 ft
--------------------------	---------------------------	--------------	----------	-------------	--------

Dust/Snow Mitigation Plan: Surface is composed of asphalt, concrete or gravel.

Est. Use Hours	8.00	Vendor	Guardian Helicopters
Contract	PSPS GUARDIAN (AS350B2)	Over Water	No
Fuel Truck	Yes	Cargo Weight	500.0 lbs
Special Equipment	HEC Gear	Billing Number	31514438 100%
Comments	My contact at DCPD is Andy Borders (805-545-3347) he will be contacting the appropriate people in the plant that there will be an aircraft in the area working but Diablo Security will still need to be notified.	Req. Notifications	Diablo -Nuclear / Powerplant

Talk About #	108	Talk Group	3363	Talk Radio #	3363
CC Recipients	J4CH@PGE.COM;JPPB@PGE.COM				

21-01861 - August 2021

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
1	2	3	4	5	6	7
8	9	10	11	12	13	14
15	16	17	18	19	20	21
22	23	24	25	26	27	28
29	30 08:30 -16:30 AS350B2 Upper Los Baros LZ 35 06.76'N 120 31.19'W	31 08:30 -16:30 AS350B2 DCPP LZ 35 12.74'N 120 49.69'W				
5	6	7	8	9	10	11



SECTION 7

Part 135 GH 4A Part 133 GH 4L

NON- Congested Area Plan

Operator: Guardian Helicopters, Inc
67 D STREET
Fillmore CA. 93015

Phone (818) 442-9904

FAX (818) 442-9901

PROJECT: PG&E POLE SET WORK ORDER #: 21-01861ADDRESS: HWY 101 CITY: NIPOMO STATE: CA.ADDRESS: PECHO CYN RD CITY: AVILIA BEACH STATE: CA8-30 LZ 35° 6'45.21"N 120°31'11.81"W26-112 120°31'11.81"W 120°31'33.14"W24/108 35° 7'51.52"N 120°32'29.07"W8-31 LZ 35°12'43.95"N 120°49'41.18"WX0/1 35°13'3.06"N 120°51'4.24"W101934800 35°13'7.38"N 120°41'54.09"W**SEE ATTACHED FLIGHT REQUEST AND KMZ FILE**CONTACT REQUESTOR: PETE DOMINGUEZ PHONE#: 805-459-6255CONTACT FORMAN: JACOB KRISTY PHONE#: 661-340-5833

PILOT'S NAME(S):

1. JOHN OLSON CERT #: 2769166
2. BUCKEY MACKAY CERT #: 2778051
3. MICHAEL KLINK CERT#: 3018828
4. IAN GOODALE CERT#: 3741973
5. ROSS GOULET CERT#: 3396777

TYPE OF AIRCRAFT: BELL UH-1H N# N777GH A/C CATEGORY: RESTRICTED
BELL 407 N# N407GH A/C CATEGORY: STANDARD
BELL 407 N# N447GH A/C CATEGORY: STANDARD
BELL 205A1 N# N216GH A/C CATEGORY: STANDARD
AS350 B2 N# N498PT A/C CATEGORY: STANDARD
AS350 B3 N# N718GH A/C CATEGORY: STANDARD
AS350 B3 N# N215GH A/C CATEGORY: STANDARD

IF SAFETY DICTATES AND OR THE CUSTOMER REQUESTS ADDITIONAL LIFTS THE LIFTS WILL BE CONDUCTED REMAINING WITHIN THE APPROVED TIME PARAMETERS.

TYPE OF LIFTS: 50 CL1' 2400 LBS ROCK 1000 LBS LOAD: EXT CL B TYPE OF ITEM LIFTING: ☐AERODYNAMIC ☒ NON- AERODYNAMIC LONG LINE: (NO) XXX (YES) LESS 150 FT (LENGTH)OPERATIONAL ALTITUDE: < 250 AGL STREET CLOSING: (NO) XX (YES)

DATE AND TIMES OPERATION WILL BEGIN AND TERMINATE:

FLIGHT DATES	TIME BEGIN	TIME END	TODAY'S DATE
8-30-2021	SUNRISE	SUNSET	8-18-2021
8-31-2021	SUNRISE	SUNSET	8-15-2021
<u>AGENCY NAME:</u>	<u>PHONE#:</u>	<u>PERSON NOTIFIED:</u>	<u>DATE:</u>
SLO POLICE DEPARTMENT	805-781-7317	DISPATCH	NOTIFIED
SLO FIRE DEPARTMENT	805-781-7380	DISPATCH	NOTIFIED



Part 135 GH 4A Part 133 GH 4L

Evacuation

Crowd Control

Street Closure

☒ No Evacuated Structures

☒ Operator

☐ Yes ☒ No

☐ Evacuated Structures

☒ Contractor

☒ Contractor

☐ Operator

LIST OF BUILDINGS THAT SHALL EITHER BE PARTIALLY OR ENTIRELY UNOCCUPIED PERSONS ALSO HOMES THAT WILL BE NOTIFIED OF ACTIVITY:

BUILDING DESCRIPTION/ADDRESS	REMARKS	METHOD
ONE STRUCTURE NEAR LZ STAGING AREA	VACANT DURING OPS	HAND DELIVER
ALL HOMES WITHIN RED OPERATING AREA	VACANT DURING OPS	HAND DELIVER
SEE DIAGRAM = VACANT	VACANT DURING OPS	HAND DELIVER

Narrative description of pick-up site, route, delivery site, and plan for ceasing operation if unauthorized persons enter operational area or real hazard occurs.

SITE INSPECTION NOTES

ONLY PERSONNEL ESSENTIAL TO COMPLETING THE JOB SAFELY WILL BE PERMITTED TO PARTICIPATE IN THE EVOLUTION. ONLY PERSONNEL PARTICIPATING IN THE SAFETY BRIEF WILL BE PERMITTED TO BE IN THE AREA OF OPERATIONS. ONLY AUTHORIZED ESSENTIAL PERSONAL WILL BE PERMITTED IN THE IMMEDIATE AREA OF OPERATIONS. IN THE EVENT AN UNAUTHORIZED PERSON ENTERS THE OPERATIONS AREA OR A POTENTIAL HAZARD IS IDENTIFIED THE PILOT WILL HOLD THE AIRCRAFT IN RELATIVE POSITION. THIS WILL BE ACHIEVED WITHOUT OVER FLYING THE GROUND CREW. ALL OPERATIONS WILL BE CEASED UNTIL THE PROBLEM IS RECTIFIED. IN THE EVENT OF AN AIRCRAFT EMERGENCY, THE PILOT WILL RADIO GROUND PERSONNEL AND WILL ATTEMPT TO LAND IN THE EMERGENCY LANDING AREA.

DURING THE LIFT EVOLUTION THE AIRCRAFT AND GROUND CREW WILL ALL BE IN RADIO COMMUNICATIONS. IN THE EVENT OF LOSS COMMUNICATIONS, THE CREW WILL USE STANDARD HAND SIGNALS TO COMMUNICATE WITH THE PILOT. WHEN THE PILOT IS CLEAR HE WILL MOVE THE AIRCRAFT TO A SAFE LOCATION TO ALLOW THE COMMUNICATION PROBLEM TO BE RECTIFIED.


THE OPERATIONS AREA IS WITHIN THE SECURED AREA. ALL ESSENTIAL CREW WITHIN THE OPERATIONS AREA WILL NOT BE INVOLVED IN TAKING PICTURES OR ANY OTHER USE OF CELL PHONES.

PRIOR TO BEGINNING OPERATIONS, A TAILBOARD SAFETY BRIEF WILL BE CONDUCTED.

1. HELICOPTER WILL LAND AT LZ TO CONDUCT TAILBOARD AND HEC TRAINING
2. WATER TRUCK IS REQUIRED AT LZ
3. EQUIPMENT AND FLYERS WILL BE LIFTED FROM LZ
4. NO STREET CLOSURES
5. ALL BUILDINGS WITHIN 300 FT OF STRUCTURE OR FLIGHT PATH SEE DIAGRAM BELOW
6. CONTRACTOR WILL PROVIDE TREE TRIMMING AS REQUIRED

LEGEND

SITE PLAN SYMBOLS: EVACUATION FLIGHT PATH		
LANDING AREA = (LZ)	STREET BLOCKED = XXXX	TOP TWO FLOORS = UBT2
ATTACH AREA = (A)	RELEASE AREA = (R)	
FLIGHT PATH = >>>	EMERGENCY LAND = (ELZ)	
UNOCCUPIED BUILDING = (UB)	UNOCCUPIED BUILDING TOP FLOOR = (UBT1)	

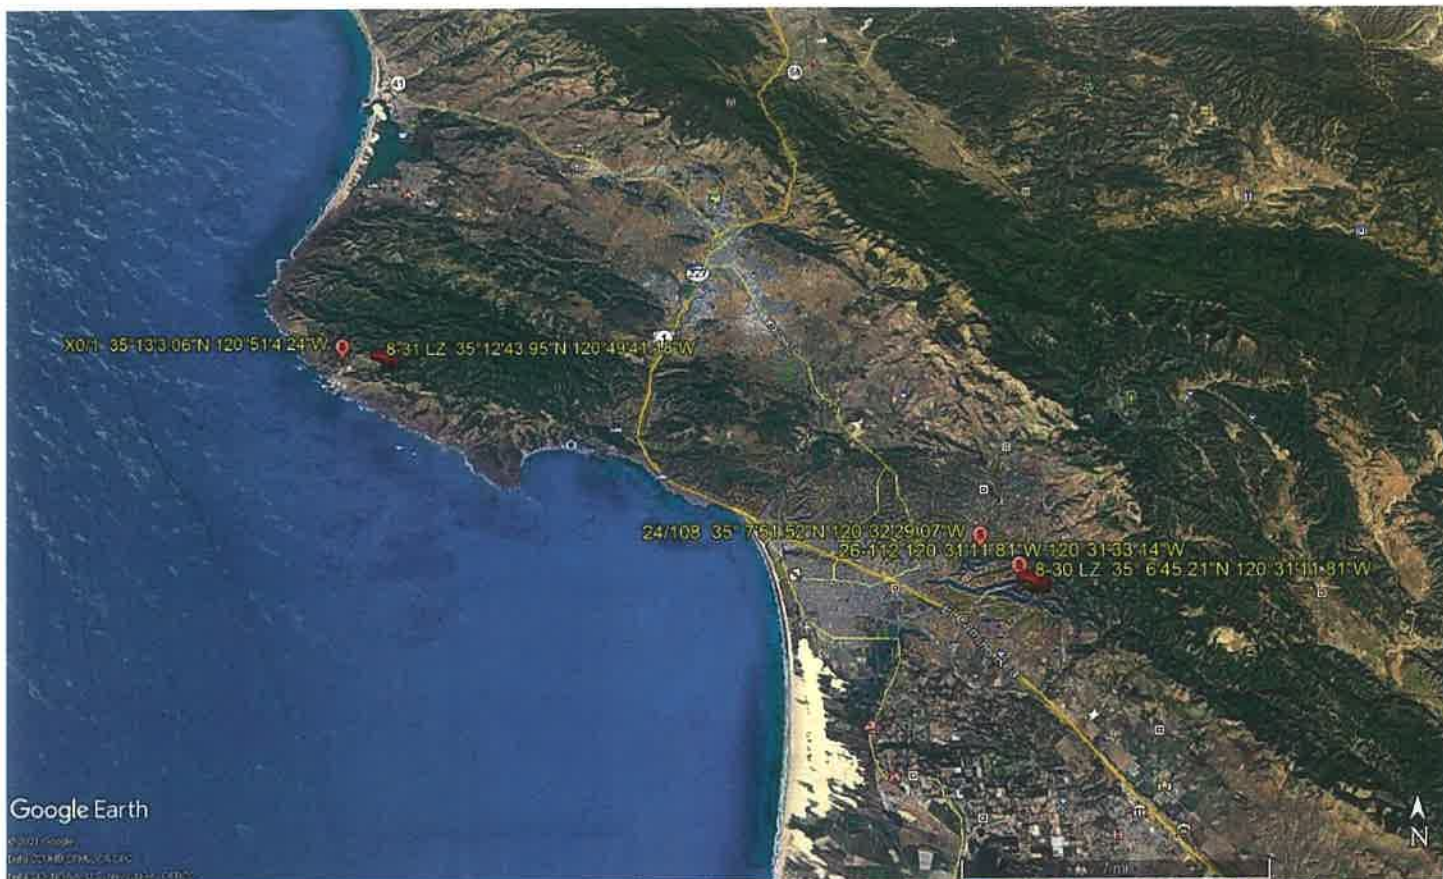



8-19-2021

DATE OF SUBMISSION

Jeffrey M. Teubner

COMPANY OFFICIAL / TITLE

Jeffrey M. Teubner Flight Coordinator
