

SCE Aircraft Operations Flight Request Form

Instructions: Please complete this form in its entirety and email to: airops@sce.com or fax to 909-974-4678. Once this form is received by Aircraft Operations, you will receive a response within 24 hours. For questions call SCE Aircraft Operations Dispatch at PAX 11676.

Requestor Information

Flight requested by:*	JOHN WHARTON
Department:*	DIVERSIFIED UTILITY SERVICES
Pax:*	00000
Cell Number:*	661 864-6051
Email Address:*	whartonj@duis1.com

SAP Accounting Number*	TD1314693 / TD1334483 / TD1282399 -BEAR VALLEY
-------------------------------	--

Flight Description

Please choose a mission type:

- | | | |
|---|--------------------------------------|---|
| ☐ Camera – HD/IR | ☐ Line String | ☒ Pole-set |
| ☐ Crew support | ☐ Passenger | ☐ Recon |
| ☐ External Load | ☐ Patrol | ☐ Training |
| ☒ HEC | ☐ Photo | ☐ Need more info, please contact |

Mission specific details (ex: Passenger name, pole size/weight, external load type, etc):

R&R 9 Det poles IN THE MOUNTAIN HOME CREEK RD SEE ATTACHED SHEET
FOR POLE NUMBERS AND WEIGHTS

General Operating Location	S/S Mountain Home Crk rd 2578' NE/O hwy 38 MTN HME VILLAGE
District	REDLANDS 31#
LZ Coordinates (if known)	N34 05 42.93 W116 56 49.20
Pick-up location for passenger flights	
Drop-off location for passenger flights	

Date(s) for which service is requested	JUNE 11 2019
Time of Pick-up	0730 AM
Approx. mission duration (if known)	0600--1600
Back-up date for mission (if known)	

Authorizer	PAUL WILLIAMSON SCE PGS
Authorizer PAX and cell number	909 557-0086

**required information*

[Click to e-mail form](#)

For office use only

Date Received by Aircraft Operations: _____ Date Initial Contact Made: _____

Referred to contractor: ☐ No ☐ Yes, Date: _____ Company: _____

Follow up status: ☐ Week 1 _____

☐ Week 2 _____

☐ Week 3 _____

BEAR VALLEY DET POLE REPLACEMENTs FOR HELICOPTER JUNE 11 2019

1. 1609676E 50' CL-4 (wt: 1259 lbs) TD1334483
2. 1609678E 50' CL-1 (wt: 1974 lbs) TD1018866
3. 1609681E 50' CL-1 (wt:1974 lbs) TD1417014
4. 4823102E 50' CL-2 (wt: 1652 lbs) TD1296914
5. 4909708E 45' CL-4 (wt: 1078 lbs) TD1282399
4909709E 45' CL-4 (wt: 1078 lbs) " "
4909710E 50' CL-4 (wt: 1259 lbs) " "
6. 1609146E 40' H-2 (wt: 1828 lbs) TD1329458
7. 1609145E 40 H-2 (WT:1828 lbs) " "

LZ N34 05 42.93 W116 56 49.20

PK UP POINT LZ FOR POLES 34.099131 -116.983462

JOHN WHARTON G.F. 661 864-6051

DIVERSIFIED UTILITY SERVICES

TR: 3/C 1/0A-33KV
TR: 3/C 4BC-12KV (SW)
TR: 2/C 4BC-12KV (SE)
TR: 1-9/32" SG (NE)
TR: 1-CATV (RENTER)
TR: 1-CATV DG (RENTER)

SET 1' NORTHEAST
POLE

1764113E
Class C3

50' Class C3
IN: 1- POLE 50' CLASS 3 WOOD FULL TREAT
IN: 3- XA SNGL FB 10' STEEL PINS
IN: 3- INS POLY W/PIN 33KV CLMP #4-653 ACSR
IN: 1- INS POLY W/PIN 12KV CLMP #6-4/0 CU
IN: 5- INS POLY DE 12KV RIG #4
IN: 2- AG DOWN GUY 9/32" - 50' LESS THAN TEST
IN: 1- AG ANCHOR ROD 1" X 10' 3-EYE W/PLATE
IN: 1- MISC AVIAN HOOD FOR HENDRIX INSUL #4-653

1764113 E
TD1314693

HFIA 12.31.18

TIER: 3


SUP

SPECIAL USE PERMIT



**SOUTHERN CALIFORNIA
EDISON**
An EDISON INTERNATIONAL Company

NOT TO SCALE

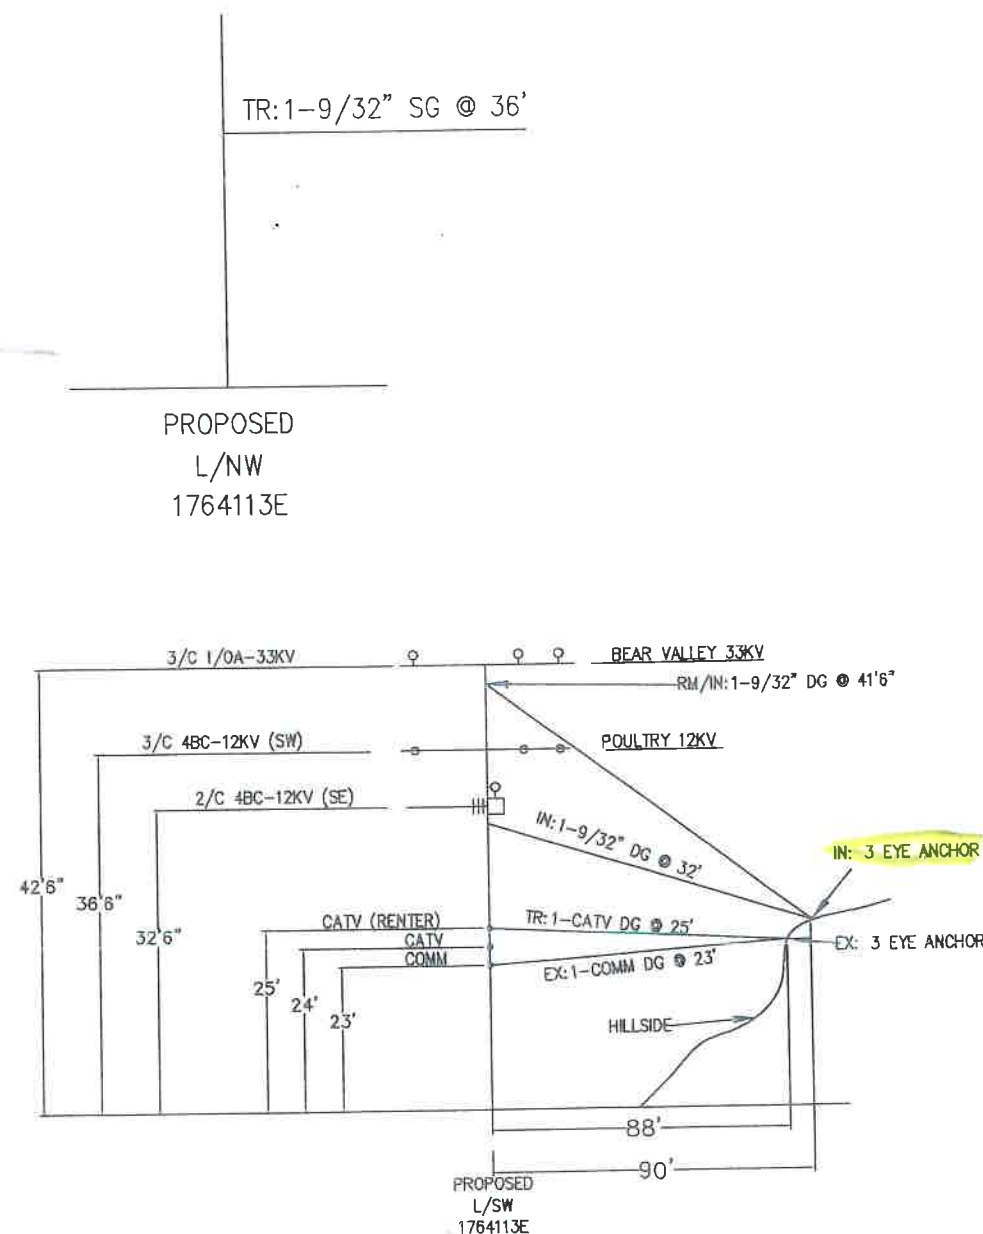

PROJECT REQUIREMENTS (Y/N)

EDISON EASEMENT REQUIRED	<u>Y</u>
PWRD 88 REQUIRED	<u>N</u>
PERMIT REQUIRED	<u>Y</u>

PERMIT TYPE:

OUTAGE REQUIRED

OUTAGE DATE: _____ TIME: _____

TRAFFIC CONTROL REQUIRED ☒ Y

PED. TRAFFIC CONTROL REQ'D ☒ N

CONVEYANCE LETTER REQ'D

ENVIRONMENTAL CLEARANCE REQ'D ☒ Y

CSD 140 (TLM) REQ'D ☐ N

D124: Rev. 04/19/16

DISTRICT 31 - REDLANDS		PROJ. MGR. SANDOVAL, SANDRA PHONE 909-660-1362		PLANNER HAMPTON TEDDER PHONE 909-628-1253		DESIGNER HAMPTON TEDDER	
PROJECT NO. 1489078		SERVICE REQUEST 2402371		MSR NO.		PRODUCT-1 1314693-INFRA REPLAC - DET POLE REPLACEMENT	
CIRCUIT / VOLTAGE BEAR VALLEY 33KV/POULTRY 12KV		THOMAS GUIDE		PRODUCT-2		ASSOC DES	
SUB / PG NO. ZANJA SUB/YUCAIPA SUB		CIRCUIT CODE 01338/14372		PRODUCT-3		ASSOC DES	
INVENTORY MAP 220-2298-2		J.P.A. NO. E6031-408845468		PROPOSED CONSTRUCTION (LOCATION) 1764113E MOUNTAIN HOME CREEK RD S/S, 2578' NE/O HWY 38 MOUNTAIN HOME VILLAGE, CA 92373			
9/29/17		PN/HTE					
TYPE DATE APPROVED BY CHECKED BY DRAWN BY PAX #		SHEET 1 OF 1		DESIGN\DRWG NO. 964476_0.01			

1609676E
TD 1334483

EDISON EASEMENT REQUIRED	☐	N
PWRD 88 REQUIRED	☐	N
UG CIVIL ONLY WORK ORDER	☐	N
PERMIT REQUIRED	☐	N

OUTAGE REQUIRED ☒ NTRAFFIC CONTROL REQUIRED ☒ N

PED. TRAFFIC CONTROL REQ'D ☒ N

CONVEYANCE LETTER REQ'D ☒ N

ENVIRONMENTAL CLEARANCE REQ'D ☒ YCSD 140 (TLM) REQ'D ☒ N

1 RM 1609676E
45' 1967
RM: 1- POLE 45' CLASS 4 WOOD FULL TREAT
RM: 2- XA SNGL VB 10' STEEL PINS
RM: 8- INS GLASS/POLY 35KV & LESS
RM: 1- AG DOWN GUY 9/32" - 50' MORE THAN 22.5KV (270')
RM: 1- AG DOWN GUY 9/32" - 50' MORE THAN 22.5KV (20')

RM: 1- 9/32" DOWN GUY
IN: 1- 3/8" DOWN GUY

RM: 1- 9/32" DOWN GUY
IN: 1- 9/32" DOWN GUY

609684E
1609677E


2 POLE 1609676E
50' Class C4
IN: 1- POLE 50' CLASS 4 WOOD FULL TREAT WT. (250)
IN: 6- INS POLY DE 33KV HOT #4 & 1/0 ACSR
IN: 2- INS POLY W/PIN 33KV CLMP #4-336 WRACSR
IN: 2- XA DBLE VB 10' STEEL PINS
IN: 1- AG DOWN GUY 9/32" - 50' MORE THAN 22.5KV (270°)
IN: 1- AG DOWN GUY 3/8" - 50' MORE THAN 22.5KV (20°)

UNDERGROUND SERVICE ALERT

Dial 811

Call USA

For Underground Locating
2 Working Days Before You Dig

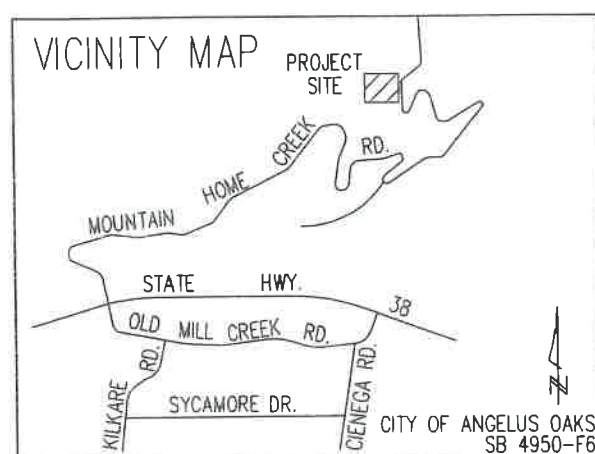

DISTRICT 31 - REDLANDS				PROJ. MGR. PHONE		PLANNER HOGUE, MICHAEL PHONE 909-307-6836		DESIGNER MOWERY, CHRISTOPHER	
PROJECT NO. 1514444		SERVICE REQUEST 2426075		MSR NO.		PRODUCT-1 1334483--INFRASTRUCTURE REPLACEMENT PLP			
CIRCUIT / VOLTAGE BEAR VALLEY 33KV		THOMAS GUIDE SB 4950--F6		PRODUCT-2				ASSOC DESGN	
SUB / PG NO. ZANJA		CIRCUIT CODE		PRODUCT-3				ASSOC DESGN	
INVENTORY MAP 220-2304-2		J.P.A. NO. E6031-409277110		PROPOSED CONSTRUCTION (LOCATION) REPLACE DET POLE VARIOUS LOCATIONS (LOCATION 1) ANGELUS OAKS (TIER 3)					
TYPE		DATE		APPROVED BY		CHECKED BY		DRAWN BY	
PAX #		SHEET 1		OF 2		DESIGN\DRWG NO. 981319 0.01			
Southern California Edison Company									

- NOTES:
- RENTER - CHARTER COMMUNICATIONS
 - POLE LOCATED ON A MOUNTAIN NEAR A WALKING TRAIL
 - NO VEHICLE ACCESS - CHOPPER SET RECOMMENDED

BULLETIN 322: ☒ Y
EAGLE ZONE: ☒ Y

TREE TRIMMING REQUIRED:
TR COMM:
PULLING ROUTINE:
SPECIAL AGREEMENT:
ADDITIONAL NOTES:

STATIONS
01 & 02

1609678E
TΔ1016866

SUP

SPECIAL USE PERMIT



NOT TO SCALE

UC SYNERGETIC
Innovative Thinking. Engineered Solutions.

GPS COORDINATES

34° 06' 27.54"
-116° 59' 24.14"

ELEVATION 4176'

HEAVY LOADING ☒ Y

ENVIRONMENTAL SCREENING
REQUIRED?

YES ☒ X

NO ☐

0121: Rev. 03/20/15

PROJECT REQUIREMENTS

EDISON EASEMENT REQUIRED ☐ N

PWRD 88 REQUIRED ☐ N

PERMIT REQUIRED ☒ Y

PERMIT TYPE: FEDERAL LAND - FOREST

OUTAGE REQUIRED ☐ N

TRAFFIC CONTROL REQUIRED ☐ N

PED. TRAFFIC CONTROL REQ'D ☐ N

PAVEMENT REPAIR REQ'D ☐ N

ASPH ☒ N CONC ☒ N SIZE -

POLE DETAILS

JOINT POLE: ☒ Y

RENTER: ☒ Y

MITC FUME: ☐ N

JOINT MEET: ☐ N

TRUCK ACCESS: ☐ N

HAND SET: ☐ N

CONTACT CATV: ☒ Y

DISTRICT 31 - REDLANDS		PROJ. MGR. RODRIGUEZ, JOHN T PHONE 626-437-9352		PLANNER MACHARIA, ROBERT K PHONE 909-608-7486		DESIGNER FITZSIMMONS, TIMOTHY J	
PROJECT NO. 1090918	SERVICE REQUEST 2012254	MSR NO.		PRODUCT-1 1016866-INFRASTRUCTURE REPLACEMENT PLP		ASSOC DESGN	
CIRCUIT / VOLTAGE BEAR VALLEY_33KV		THOMAS GUIDE N/A		PRODUCT-2		ASSOC DESGN	
SUB / PG NO. ZANJA		CIRCUIT CODE		PRODUCT-3		ASSOC DESGN	

INVENTORY MAP 220-2304-2		J.P.A. NO.		PROPOSED CONSTRUCTION (LOCATION) DET POLE REPLACEMENT (1609678E) 8171 MOUNTAIN HOME CREEK RD REDLANDS, CA			
TYPE	DATE	APPROVED BY	CHECKED BY	DRAWN BY	PAX #	SHEET	DESIGN/DRWG NO. 712078_0.01
Southern California Edison Company							OF

NOTE:

HARD SET N.W

POLE

1609678E

2

50' Class C1
IN: 1- POLE 50' CLASS 1 WOOD FULL TREAT
IN: 1- XA DBLE VB 10' STEEL PINS
IN: 6- INS POLY DE 33KV HOT #4 & 1/0 ACSR
IN: 1- INS POLY W/PIN 33KV CLMP #4-653 ACSR
IN: 2- AG DOWN GUY 3/8" - 50' MORE THAN 22.5KV

12' LEAD

MOUNTAIN HOME CREEK RD

1609677E

⊕ ⊕ 45

1609684E

45

1

RM

1609678E


45' Class C4
RM: 1- POLE 45' CLASS 4 WOOD FULL TREAT
RM: 1- XA DBLE VB 10' STEEL PINS
RM: 6- INS POLY DE 33KV HOT #4 & 1/0 ACSR
RM: 1- INS POLY W/PIN 33KV CLMP #4-653 ACSR
RM: 2- AG DOWN GUY 9/32" - 50' MORE THAN 22.5KV

NOTE:

TR: (3) 1/0ACSR - 33KV PRIMARY


TR: (1) ANCHOR

RISER - DETAIL




GUY - DETAIL

FACING NORTH

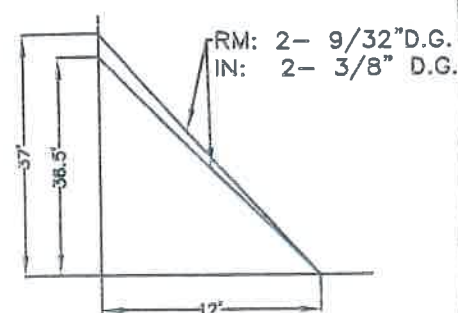

VICINITY MAP

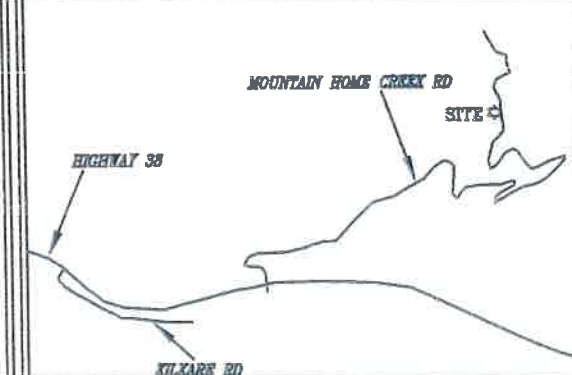

*** NOTES:**




HIGH FIRE - 3
RENTER - CONTACT CATV
ENVIRO POLE - WOODPECKER
FEDERAL LAND - US FOREST SERVICE
BULLETIN 322 AREA
E-ALL POLE
COMPOSITE POLE

HARD ACCESS: OFF OF A WASHED UP DIRT ROAD WITH NO TRUCK
ACCESS. BEHIND LOCKED GATE.


HAND SET
RIGHTS CHECK REQ'D - FEDERAL LAND

TR: 3/C 1/0A-33KV(NE)

TR: 3/C 1/0A-33KV(SE)

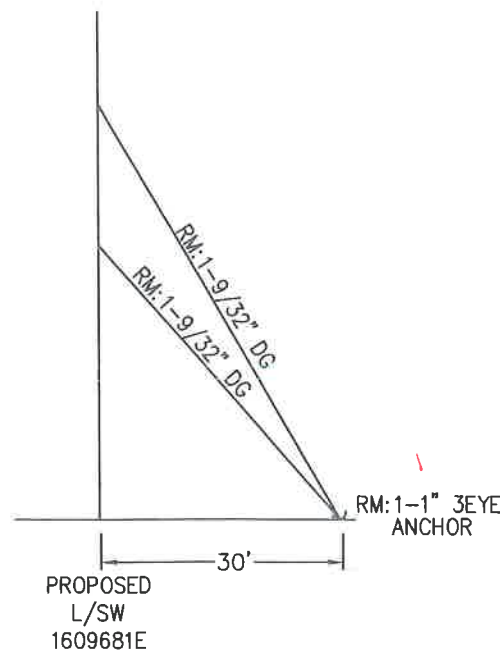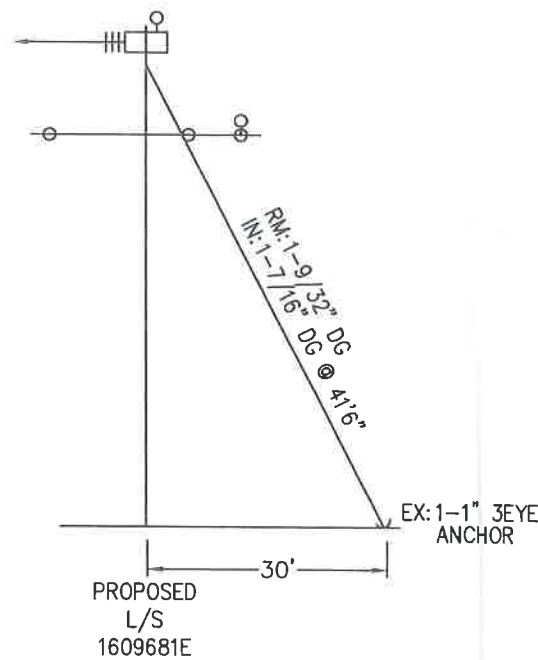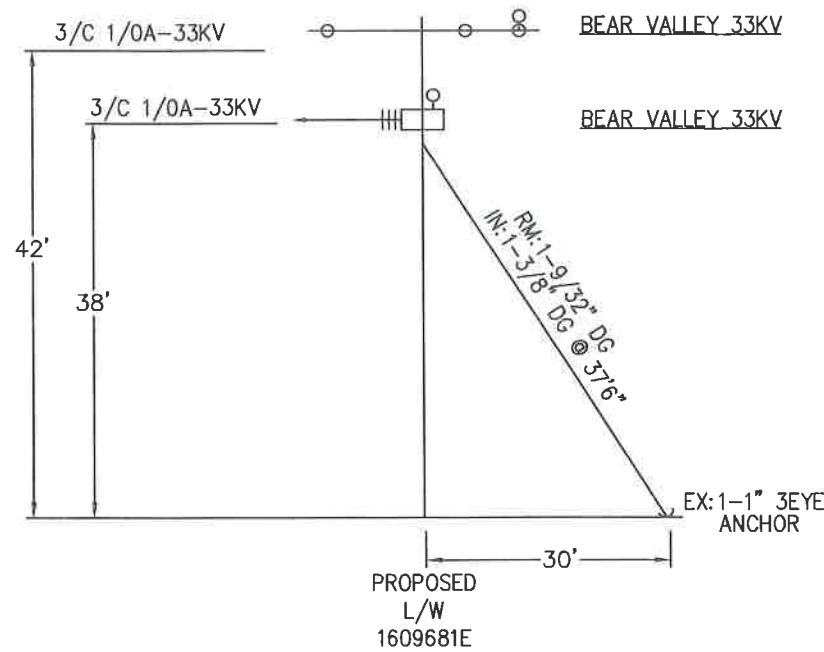

- 1 RM 1609681E Class C4
- RM: 1- POLE 50' CLASS 4 WOOD FULL TREAT
 - RM: 2- XA DBLE VB 10' STEEL PINS
 - RM: 2- INS GLASS & PIN 33KV CLMP #4-336 ACSR
 - RM: 6- INS PORC DE 33KV HOT SHOE #4 & 1/0 ACSR
 - RM: 4- AG DOWN GUY 9/32" - 50' LESS THAN 22.5KV
 - RM: 1- AG ANCHOR ROD 1" X 10' 3-EYE W/PLATE

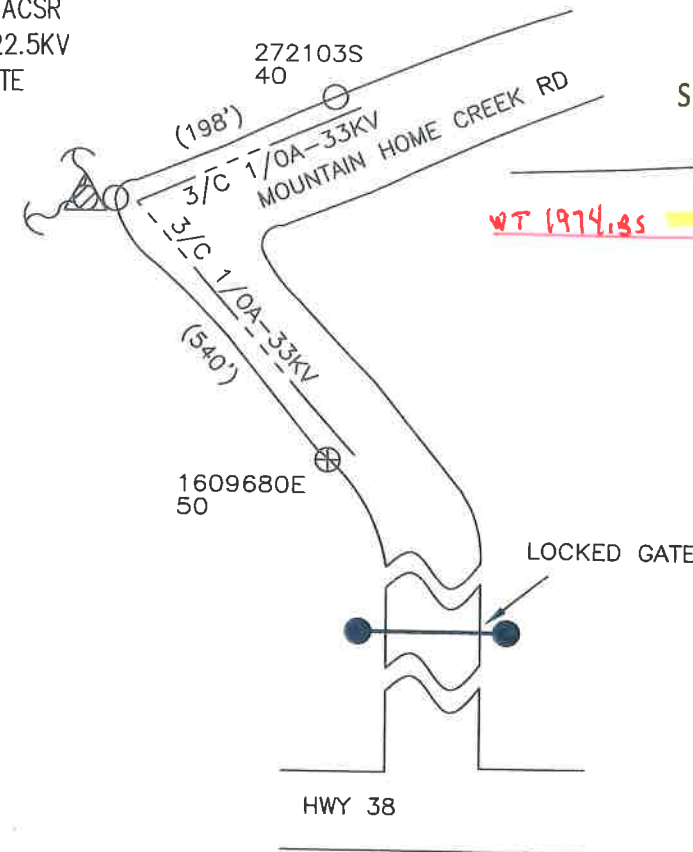

SET 1' EAST
POLE

- 2 1609681E Class C1
- IN: 1- POLE 50' CLASS 1 RS COMP SEC POLE
 - IN: 4- CROSSARM, COMPOSITE, DEADEND, HEAVY DUTY, 10' LENGTH
 - IN: 2- ATTACHMENT, GUY, DUCTILE IRON
 - IN: 2- INS POLY W/PIN 33KV CLMP #4-653 ACSR
 - IN: 6- INS POLY DE 33KV HOT SHOE #4 & 1/0 ACSR
 - IN: 1- AG DOWN GUY 7/16" - 50' LESS THAN 22.5KV
 - IN: 1- AG DOWN GUY 3/8" - 50' LESS THAN 22.5KV

N: 34° 6' 40.98"
W: 116° 59' 28.10"
ELEVATION: 4273'

HFIA 4.19.19

TIER: 3



NOT TO SCALE

SECTIONAL COMPOSITE

PROJECT REQUIREMENTS (Y/N)

- EDISON EASEMENT REQUIRED ☐
- PWRD 88 REQUIRED ☐
- UG CIVIL ONLY WORK ORDER ☐
- PERMIT REQUIRED ☒
- PERMIT TYPE: _____
- OUTAGE REQUIRED ☐
- OUTAGE DATE: _____ TIME: _____
- TRAFFIC CONTROL REQUIRED ☐
- PED. TRAFFIC CONTROL REQ'D ☐
- CONVEYANCE LETTER REQ'D ☐
- ENVIRONMENTAL CLEARANCE REQ'D ☐
- CSD 140 (TLM) REQ'D ☐

D124: Rev. 02/08/18

DISTRICT 31 - REDLANDS	PROJ. MGR. SANDOVAL, SANDRA PHONE (909) 660-1362	PLANNER HAMPTON TEDDER PHONE (909) 628-1253	DESIGNER HAMPTON TEDDER
PROJECT NO. 1616440	SERVICE REQUEST 2525020	MSR NO.	PRODUCT-1 1417014-INFRA REPLAC - DET POLE REPLACEMENT
CIRCUIT / VOLTAGE BEAR VALLEY 33KV	THOMAS GUIDE	PRODUCT-2	ASSOC DESGN
SUB / PG NO. ZANJA SUB	CIRCUIT CODE 01338	PRODUCT-3	ASSOC DESGN
INVENTORY MAP 224-2304-2	J.P.A. NO.	PROPOSED CONSTRUCTION (LOCATION) 1609681E MOUNTAIN HOME CREEK RD W/S, .72MI N/O HWY 38 MENTONE, CA	
10/31/18	SL/HTE	SHEET 1 OF 1	
TYPE	DATE	APPROVED BY	DESIGN\DRWG NO. 10486.32 001
Southern California Edison Company			

PROJECT REQUIREMENTS (Y/N)

EDISON EASEMENT REQUIRED ☐ N

PWRD 88 REQUIRED ☐ Y

PERMIT REQUIRED ☐ N

PERMIT TYPE: N/A

OUTAGE REQUIRED ☐ N

OUTAGE DATE: N/A TIME: _____

TRAFFIC CONTROL REQUIRED ☐ N


PED. TRAFFIC CONTROL REQ'D ☐ N

CONVEYANCE LETTER REQ'D ☐ N

ENVIRONMENTAL CLEARANCE REQ'D ☐ Y

CSD 140 (TLM) REQ'D ☐ N

NO ENVIRONMENTAL

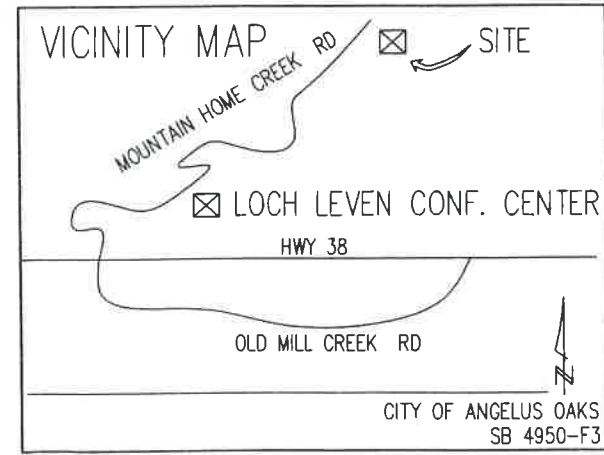

DISTRICT 31 - REDLANDS				PROJ. MGR. PHONE		PLANNER SALMON, DAVID A PHONE 909-307-6710		DESIGNER SINGH CORRAL, JENNIFER	
PROJECT NO. 1465496		SERVICE REQUEST 2379329		MSR NO. N/A		PRODUCT-1 4296914		INFRA REPLAC - DET POLE REPLACEMENT	
CIRCUIT / VOLTAGE BEAR VALLEY				THOMAS GUIDE SB 4950-F3		PRODUCT-2		ASSOC DESIGN	
SUB / PG NO. ZANJA				CIRCUIT CODE		PRODUCT-3		ASSOC DESIGN	
INVENTORY MAP 224-2304-2				J.P.A. NO. N/A		PROPOSED CONSTRUCTION (LOCATION) DETERIORATED POLE REPLACEMENT 2385' N, 2475' W FR. S/E COR OF SEC 4 TIS R/W ANGELUS OAKS, CA 92305 NOTIFICATION #: 405688405			
TYPE	DATE	APPROVED BY	CHECKED BY	DRAWN BY	PAX #	SHEET 1 of 1		DESIGN\DRWG NO. 950312_0.01	
Southern California Edison Company									

*** NOTES:**

ENVIRO POLE - OPEN SPACE / WOODPECKER
FEDERAL PERMIT REQ'D - SAN BERNARDINO NATIONAL FOREST
CREW NOTE: INSTALL 50' POLE FOR POLE

4909710E, BASE OF POLE IS LOWER
THAN RELATED POLES. ON SLOPE OF HILL.





BULLETIN 322 AREA

E-ALL POLE

HAND SET

HELICOPTER SET REQ'D

TR: 3/C 1/0A-33KV

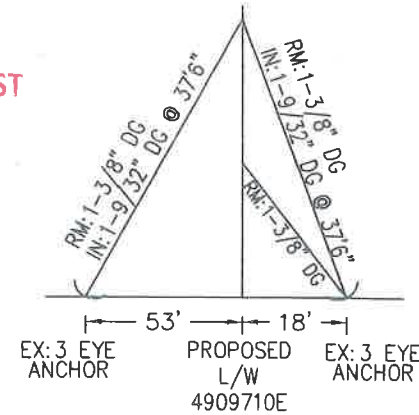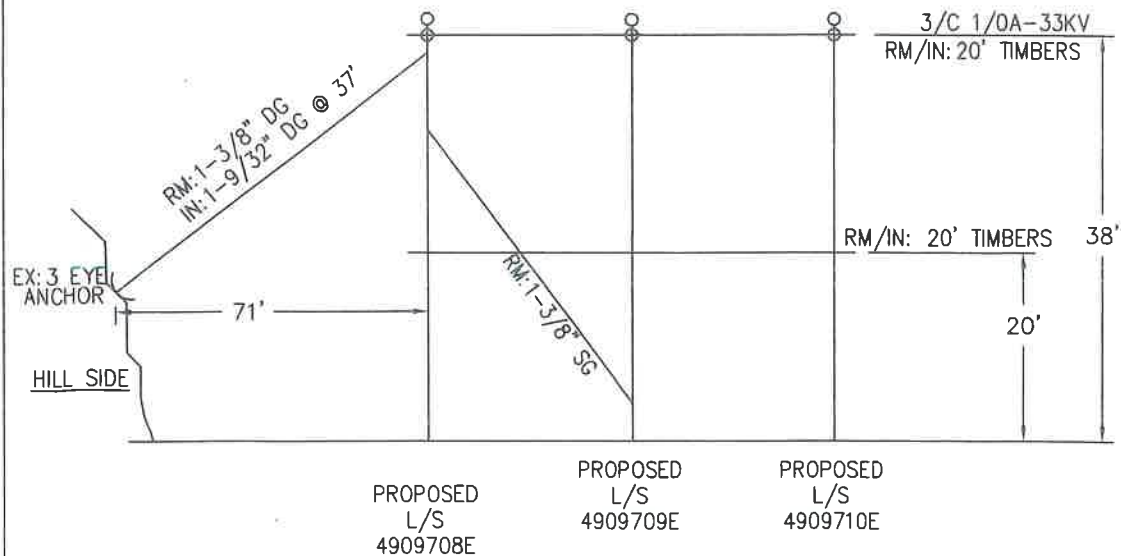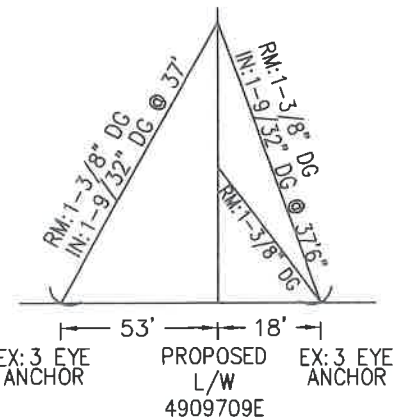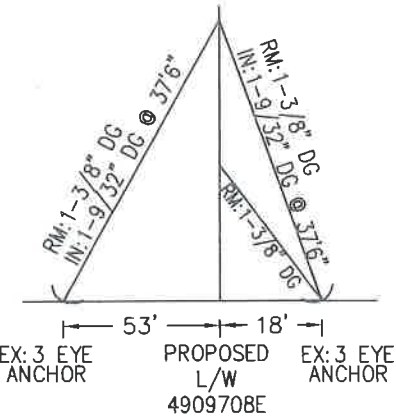

- 1 RM 272107A Class C2
45'
RM: 1- POLE 45' CLASS 2 WOOD FULL TREAT
RM: 3- SA PORC 33KV 1-EA
RM: 2- XA DBLE H FRAME 20' SUSP OR DE W/X FRM
RM: 3- INS POST PORC 33KV UCLMP #4-336 ACSR
RM: 6- INS PORC DE 33KV HVY LOAD #4 & 1/0 ACSR
RM: 10- AG DOWN GUY 3/8" - 50' MORE THAN 22.5KV
RM: 1- AG SPAN GUY 3/8" - 200'

- 3 RM 272107B Class C2
45'
RM: 1- POLE 45' CLASS 2 WOOD FULL TREAT

- 5 RM 272107C Class C2
45'
RM: 1- POLE 45' CLASS 2 WOOD FULL TREAT

DESIGN NOTE: 50' IN FIELD

PROJECT REQUIREMENTS (Y/N)

EDISON EASEMENT REQUIRED	☐
PWRD 88 REQUIRED	☐
PERMIT REQUIRED	☒
PERMIT TYPE:	
OUTAGE REQUIRED	☐
OUTAGE DATE: _____ TIME: _____	
TRAFFIC CONTROL REQUIRED	☐
PED. TRAFFIC CONTROL REQ'D	☐
CONVEYANCE LETTER REQ'D	☐
ENVIRONMENTAL CLEARANCE REQ'D	☒
CSD 140 (TLM) REQ'D	☐

DISTRICT 31 - REDLANDS	PROJ. MGR. SANDOVAL, SANDRA PHONE (909) 660-1362	PLANNER HAMPTON TEDDER PHONE (909) 628-1253	DESIGNER HAMPTON TEDDER
PROJECT NO. 1445219	SERVICE REQUEST 2359461	MSR NO. THOMAS GUIDE	PRODUCT-1 1282399-INFRA REPLAC - DET POLE REPLACEMENT
CIRCUIT / VOLTAGE BEAR VALLEY 33KV	SUB / PG NO. ZANJA SUB	CIRCUIT CODE 01338	PRODUCT-2
INVENTORY MAP 224-2304-2	J.P.A. NO.	PRODUCT-3	ASSOC DESGN
DATE 7/25/2017	APPROVED BY	CHECKED BY	DRAWN BY
TYPE	DATE	APPROVED BY	CHECKED BY
SS/HTE			
SHEET 1	OF 1	DESIGN\DRWG NO. 937933	0.01

N: 34° 6' 55.13"
W: 116° 59' 10.63"
ELEVATION: 4526'

SET 1' NORTH

POLE 4909708E

- 45'
IN: 1- POLE 45' CLASS 4 WOOD FULL TREAT
IN: 2- XA DBLE H FRAME 20' SUSP OR DE W/X FRM
IN: 3- INS POLY W/PIN 33KV CLMP #4-653 ACSR
IN: 6- INS POLY DE 33KV COLD 1/0 ACSR
IN: 7- AG DOWN GUY 9/32" - 50' MORE THAN 22.5KV

N: 34° 6' 55.15"
W: 116° 59' 10.76"
ELEVATION: 4524'

SET 1' NORTH

POLE 4909709E

- 45'
IN: 1- POLE 45' CLASS 4 WOOD FULL TREAT

N: 34° 6' 55.17"
W: 116° 59' 10.88"
ELEVATION: 4521'

SET 1' NORTH

POLE 4909710E

- 50'
IN: 1- POLE 50' CLASS 4 WOOD FULL TREAT



NOT TO SCALE

A map of the study area showing the location of the study site (marked with an 'X') relative to Angelus Oaks, Mountain Home, and Forest Falls. The map includes Old Hwy 38 and Hwy 38.

1609145E
1609146E
TD1329452

EDISON EASEMENT REQUIRED ☐

PWRD 88 REQUIRED ☐

PERMIT REQUIRED ☐

PERMIT TYPE: FORESTRY

OUTAGE REQUIRED ☐

OUTAGE DATE: _____ TIME: _____

TRAFFIC CONTROL REQUIRED ☐

PED. TRAFFIC CONTROL REQ'D ☐

CONVEYANCE LETTER REQ'D ☐

ENVIRONMENTAL CLEARANCE REQ'D ☐

CSD 140 (TLM) REQ'D ☐

N 34.118855
W. 116.982800



For Underground Locating
2 Working Days Before You Dig

- TRAMP POLE, RE-BUILD AS SEEN IN FIELD.
- HELICOPTER SET
- HAND DIG POLE HOLES N/O EXISTING STRUCTURES.
- DOWN GUYS TO RE-USE EX. ANCHORS.
- POLE IS 3 MILES S/O GATE IN ANGELUS OAKS, OR 2.5 MILES N/O LOCH LEVEN CONFERENCE CENTER.
- 34° 7' 3.48" N 116° 59' 13.88" W

DISTRICT 31 - REDLANDS				PROJ. MGR. SANDOVAL, SANDRA PHONE 909-660-1362				PLANNER DENT, MICHAEL PHONE 909-307-6874				DESIGNER L. ADAMS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																											
PROJECT NO. 1508205		SERVICE REQUEST 2420024		MSR NO. N/A		PRODUCT-1 1329458-INFRA REPLAC - DET POLE REPLACEMENT										ASSOC DESGN																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
CIRCUIT / VOLTAGE BEAR VALLEY 33KV				THOMAS GUIDE		PRODUCT-2										ASSOC DESGN																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
SUB / PG NO. ZANJA				CIRCUIT CODE		PRODUCT-3										ASSOC DESGN																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
INVENTORY MAP 224-2304-2				J.P.A. NO. E6031-408970837										PROPOSED CONSTRUCTION (LOCATION) DET POLE REPLACEMENT STR 1609145E 2.5 MILES N/O LOCH LEVEN CNFR MOUNTAIN HOME/ANGELUS OAKS NOTIFICATION #408761203																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
