



SOUTHERN CALIFORNIA
EDISON

An EDISON INTERNATIONAL® Company

SCE Aircraft Operations Flight Request Form

Instructions: Please complete this form in its entirety and email to: airops@sce.com or fax to 909-974-4678. Once this form is received by Aircraft Operations, you will receive a response within 24 hours. For questions call SCE Aircraft Operations Dispatch at PAX 11676.

Requestor Information

Flight requested by:*	Gilbert leon
Department:*	tbd/santa barbara
Pax:*	n/a
Cell Number:*	805-358 0963
Email Address:*	gilbert.leon@sce.com

SAP Accounting Number* id 1572091

Flight Description

Please choose a mission type:

- | | | |
|---|--------------------------------------|---|
| ☐ Camera – HD/IR | ☐ Line String | ☒ Pole-set |
| ☐ Crew support | ☐ Passenger | ☐ Recon |
| ☐ External Load | ☐ Patrol | ☐ Training |
| ☐ HEC | ☐ Photo | ☐ Need more info, please contact |

Mission specific details (ex: Passenger name, pole size/weight, external load type, etc):

pole set 45 ft cl 2 1425 lbs

General Operating Location	40 celine rd santa barbara
District	SB dist 49
LZ Coordinates (if known)	34.4616 -1197310 pole staged here
Pick-up location for passenger flights	n/a
Drop-off location for passenger flights	n/a

Date(s) for which service is requested	11-5-19
Time of Pick-up	1000am
Approx. mission duration (if known)	4hrs
Back-up date for mission (if known)	

Authorizer	Alicia Pillado
Authorizer PAX and cell number	75203 805-358 -8337

**required information*

[Click to e-mail form](#)

For office use only

Date Received by Aircraft Operations: _____ Date Initial Contact Made: _____

Referred to contractor: ☐ No ☐ Yes, Date: _____ Company: _____

Follow up status: ☐ Week 1

☐ Week 2

☐ Week 3



40 Celine dr.
Santa Barbara

TD 1572091


work date 11-5-19

TD1572091 WESTFALL 4KV WESTFALL P.M. SUB

CREW NOTES:

- REPLACING PCBRP TRANSFORMER
- POLE LOCATED BEHIND 40 CELINE DR. (SEE PICTURE)
- CRANE SET REQ (180' FROM CURBFACE)
- POSSIBLE TREE TRIMMING

EX: 1413509E
45'
CL 2 - 1425165
RM: 1-10 KVA XFMR 4KV 1 PHASE
RM: 1-CUTOUT W/FUSE
IN: 1-25 KVA XFMR 4KV 1 PHASE (T-0-25-2.4-5)
IN: 1-25A ELF FUSE (FE-ELF-8-25A-1)
IN: 1-ELF CUTOUT (FE-CO-2.4-3)
W: 1-45' CL 2

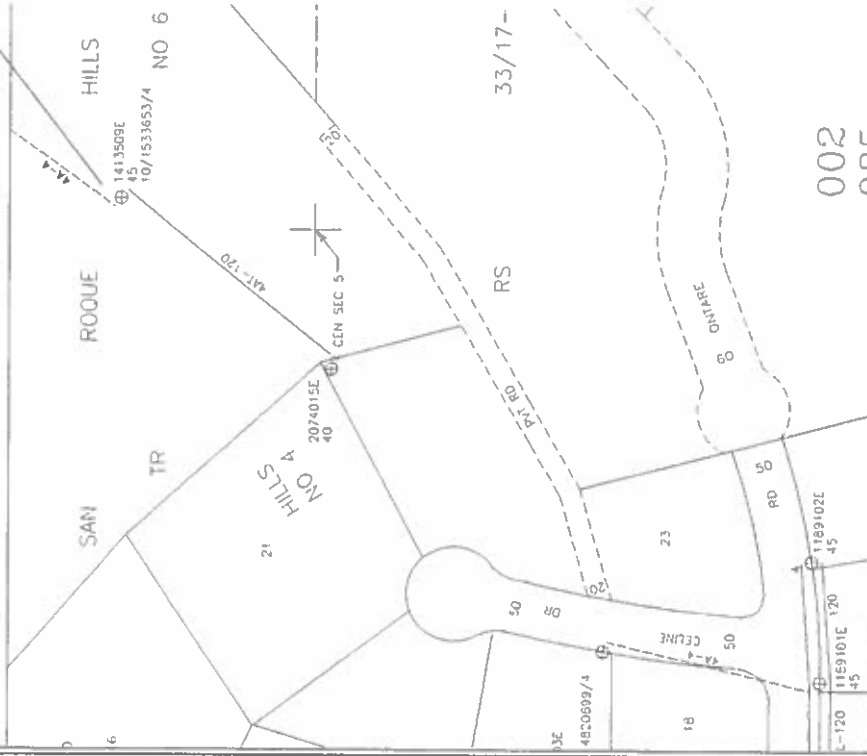

PROJECT REQUIREMENTS (Y/N)

EDISON EASEMENT REQUIRED ☐
PMRD 88 REQUIRED ☐
UG CIVIL ONLY WORK ORDER ☒
PERMIT REQUIRED ☐
OUTAGE REQUIRED ☒
OUTAGE DATE: _____ TIME: _____
TRAFFIC CONTROL REQUIRED ☐
PED. TRAFFIC CONTROL REQ'D ☐
CONVEYANCE LETTER REQ'D ☐
ENVIRONMENTAL CLEARANCE REQ'D ☐
CSD 140 (TUM) REQ'D ☐

3174 Rev 02/24/13

T.L.M. DATA:
SIZE KVA CUST % LOAD
EXIST. 10 15.8 2 157.92%
PROP. 25 15.8 2 63.20%
VOLTAGE DROP: _____
FLICKER FACTOR: _____
PRI. CIRCUIT: WESTFALL 4KV



Southern California Edison
An Edison International Company

NOT TO SCALE

DISTRICT	49-SANTA BARBARA	PRGAL NO.	PRGAL PHONE	PLANNER	PHONE	DESIGNER
PROJECT NO.	SERVICE REQUEST	EST. NO.	PRODUCT-1	TD1572091		ASSOC DESIGN
CIRCUIT / VOLTAGE	WESTFALL 4KV	TRANS CODE	PRODUCT-2			ASSOC DESIGN
SUB / PM NO.	WESTFALL P.M. SUB	CIRCUIT CODE	PRODUCT-3			ASSOC DESIGN
INVENTORY MAP	18-46C	J.P.A. NO.	PROPOSED CONSTRUCTION (LOCATION)	40 CELINE DR.		
				SANTA BARBARA 8105		
TYPE	DATE	APPROVED BY	CHECKED BY	DRAWN BY	PAX #	SHEET
						1 of 1
Southern California Edison Company						

